College of Computer Studies, Engineering, and Architecture

Software Project Management Plan (SPMP)

For

ExGen Battery Center & Car Wash:Web-based Quotation & Billing System

by:

Junray T. Alfanta

Wane Summer J. Francisco

Jewel Nerisha T. Tomale

Preface

This document aims to elaborate the Software Project Management Plan (SPMP) of the JavaScript-Based Code Parser, Formatter, and Minifier whose primary users of the system are anyone in the IT industry who codes (or reads code) wherein, they can have the opportunity to format the code, allowing them to improve readability or file optimization.

The author primarily writes this document as guidance for the software project members to indicate mandatory requirements to be followed to conform to the given standard approved by the university.

Change History

Version 1, August 7, 2026

- The first draft of this document.

Version 2, September 29, 2026

- The revision of the first draft.

Table of Contents

Preface 2
Table of Contents 4
List of Figures 6
List of Tables 7
1. Overview 12
    1.1 Project Summary 12
        1.1.1 Purpose, Scope, and Objectives 12
        1.1.2 Assumptions and Constraints 13
        1.1.3 Project Deliverables 16
        1.1.4 Schedule and Budget Summary 17
    1.2 Evolution of the plan 18
2. Definitions 20
3. Project Organization 25
    3.1 External Structures (DIAGRAM) 25
    3.2 Internal Structure (DIAGRAM) 26
    3.3 Roles and Responsibilities 27
4. Managerial Process Plans 30
    4.1 Start-Up Plan 30
        4.1.1 Estimation Plan 30
        4.1.2 Staffing Plan 31
        4.1.3 Resource Acquisition Plan 33
        4.1.4 Project Staff Training Plan 35
    4.2 Work Plan 37
        4.2.1 Work Activities 37
        4.2.2 Schedule Allocation 39
        4.2.3 Resource and Budget Allocation 39
    4.3 Control Plan 39
        4.3.1 Requirements Control Plan 40
        4.3.2 Schedule Control Plan 41
        4.3.3 Budget Control Plan 42
        4.3.4 Quality Control Plan 43
        4.3.5 Reporting Plan 44
        4.3.5.1 Internal Reporting Plan 44
        4.3.6 Metrics Collection Plan 45
    4.4 Risk Management Plan 47

4.5 Closeout Plan 47
5. Technical Process Plan 49
5.1 Process Model 49
5.2 Methods, Tools, and Techniques 52
5.3 Infrastructure Plan 53
5.4 Product Acceptance Plan 54
6. Supporting Process Plans 57
6.1 Documentation Plan 57
6.2 Configuration Management Plan 58
6.3 Verification and Validation Plan 59
6.4 Quality Assurance Plan 60
6.5 Reviews and Audits 62
6.6 Problem Resolution Plan 64
6.7 Subcontractor Management Plan 66
6.8 Process Improvement Plan 66
7. Additional Plans 68
RMMM Traceability Matrix 69
References **204**
Appendices **206**
APPENDIX A 206

List of Figures

Figure 1: External Structure 25
Figure 2: The Agile Methodology 49
Figure 3: Transmittal Letter 206
Figure 4: First Meeting with the Client 207

List of Tables

Table 1: Project Schedule Summary 18
Table 2: Project Budget Summary 18
Table 3: Evolution of the Plan 19
Table 4: Roles and Responsibilities 29
Table 5: Staffing Plan 32
Table 6 : Source Catalog Details 35
Table 7: Project Staff Training Plan 37
Table 8: Work Activities 39
Table 9 : Resource and Budget Allocation 39
Table 10 : Requirements Control Plan 41
Table 11 : Schedule Control Plan 42
Table 12 : Budget Control Plan 43
Table 13 : Internal Reporting Plan 45
Table 14 : Weekly Objectives Metrics 45
Table 15 : Team Collaboration Metrics 46
Table 16 : Budget Metrics 46
Table 17 : Client Feedback Score Metrics 46
Table 18 : Quality Assurance Metrics 47
Table 19 : RMMM Traceability Metrics 47
Table 20: Methods, Tools, and Technique 53
Table 21: Infrastructure Plan 54
Table 22: Documentation Plan 58
Table 23: Configuration Management Plan 59
Table 24: Verification and Validation Plan 60
Table 25: Quality Assurance Plan 62
Table 26: Reviews and Audits Table 64
Table 27: Problem Resolution Plan 66
Table 28: Process Improvement Plan 67
Table 29: RMMM Traceability for Technical Risk 75
Table 30: RIS item No.1 Project Risks 76
Table 31: RIS item No.2 Project Risks 77
Table 32: RIS item No.3 Project Risks 78
Table 33: RIS item No.4 Project Risks 79
Table 34: RIS item No.5 Project Risks 79
Table 35: RIS item No.6 Project Risks 80

Table 36: RIS item No.7 Project Risks 81
Table 37: RIS item No.8 Project Risks 82
Table 38: RIS item No.9 Project Risks 83
Table 39: RIS item No.10 Project Risks 84
Table 40: RIS item No.11 Project Risks 84
Table 41: RIS item No.12 Project Risks 85
Table 42: RIS item No.13 Project Risks 86
Table 43: RIS item No.14 Project Risks 87
Table 44: RIS item No.15 Project Risks 88
Table 45: RIS item No.16 Project Risks 89
Table 46: RIS item No.17 Project Risks 89
Table 47: RIS item No.18 Project Risks 90
Table 48: RIS item No.19 Project Risk 91
Table 49: RIS item No.20 Project Risk 92
Table 50: RIS item No.21 Project Risk 92
Table 51: RIS item No.22 Project Risk 93
Table 52: RIS item No.23 Project Risk 94
Table 53: RIS item No.24 Project Risk 95
Table 54: RIS item No.25 Project Risk 96
Table 55: RIS item No.26 Project Risk 96
Table 56: RIS item No.27 Project Risk 97
Table 57: RIS item No.28 Project Risk 98
Table 58: RIS item No.29 Project Risk 99
Table 59: RIS item No.30 Project Risk 99
Table 60: RIS item No.31 Project Risk 100
Table 61: RIS item No.32 Project Risk 101
Table 62: RIS item No.33 Project Risk 102
Table 63: RIS item No.34 Project Risk 102
Table 64: RIS item No.35 Project Risk 103
Table 65: RIS item No.36 Project Risk 104
Table 66: RIS item No.37 Project Risk 105
Table 67: RIS item No.38 Project Risk 106
Table 68: RIS item No.39 Project Risk 106
Table 69: RIS item No.40 Project Risk 107
Table 70: RIS item No.41 Project Risk 108
Table 71: RIS item No.42 Project Risk 109
Table 72: RIS item No.43 Project Risk 109

Table 73: RIS item No.44 Project Risk 110
Table 74: RIS item No.45 Project Risk 111
Table 75: RIS item No.46 Project Risk 112
Table 76: RIS item No.47 Project Risk 112
Table 77: RIS item No.48 Project Risk 113
Table 78: RIS item No.49 Project Risk 114
Table 79: RIS item No.50 Project Risk 115
Table 80: RMMM Traceability for Technical Risk 121
Table 81: RIS item No.1 Technical Risk 121
Table 82: RIS item No.2 Technical Risk 122
Table 83: RIS item No.3 Technical Risk 123
Table 84: RIS item No.4 Technical Risk 124
Table 85: RIS item No.5 Technical Risk 124
Table 86: RIS item No.6 Technical Risk 125
Table 87: RIS item No.7 Technical Risk 126
Table 88: RIS item No.8 Technical Risk 127
Table 89: RIS item No.9 Technical Risk 128
Table 90: RIS item No.10 Technical Risk 128
Table 91: RIS item No.11 Technical Risk 129
Table 92: RIS item No.12 Technical Risk 130
Table 93: RIS item No.13 Technical Risk 131
Table 94: RIS item No.14 Technical Risk 131
Table 95: RIS item No.15 Technical Risk 132
Table 96: RIS item No.16 Technical Risk 133
Table 97: RIS item No.17 Technical Risk 134
Table 98: RIS item No.18 Technical Risk 134
Table 99: RIS item No.19 Technical Risk 135
Table 100: RIS item No.20 Technical Risk 136
Table 101: RIS item No.21 Technical Risk 137
Table 102: RIS item No.22 Technical Risk 137
Table 103: RIS item No.23 Technical Risk 138
Table 104: RIS item No.24 Technical Risk 139
Table 105: RIS item No.25 Technical Risk 140
Table 106: RIS item No.26 Technical Risk 140
Table 107: RIS item No.27 Technical Risk 141
Table 108: RIS item No.28 Technical Risk 142
Table 109: RIS item No.29 Technical Risk 143

Table 110: RIS item No.30 Technical Risk 143
Table 111: RIS item No.30 Technical Risk 144
Table 112: RIS item No.31 Technical Risk 145
Table 113: RIS item No.33 Technical Risk 146
Table 114: RIS item No.34 Technical Risk 146
Table 115: RIS item No.35 Technical Risk 147
Table 116: RIS item No.36 Technical Risk 148
Table 117: RIS item No.37 Technical Risk 149
Table 118: RIS item No.38 Technical Risk 149
Table 119: RIS item No.39 Technical Risk 150
Table 120: RIS item No.40 Technical Risk 151
Table 121: RIS item No.41 Technical Risk 152
Table 122: RIS item No.42 Technical Risk 153
Table 123: RIS item No.43 Technical Risk 153
Table 124: RIS item No.44 Technical Risk 154
Table 125: RIS item No.45 Technical Risk 155
Table 126: RIS item No.46 Technical Risk 156
Table 127: RIS item No.47 Technical Risk 156
Table 128: RIS item No.48 Technical Risk 157
Table 129: RIS item No.49 Technical Risk 158
Table 130: RIS item No.50 Technical Risk 159
Table 131: RMMM Traceability for Technical Risk 165
Table 132: RIS item No.1 Business Risk 165
Table 133: RIS item No.2 Business Risk 166
Table 134: RIS item No.3 Business Risk 167
Table 135: RIS item No.4 Business Risk 168
Table 136: RIS item No.5 Business Risk 168
Table 137: RIS item No.6 Business Risk 169
Table 138: RIS item No.7 Business Risk 170
Table 139: RIS item No.8 Business Risk 171
Table 140: RIS item No.9 Business Risk 171
Table 141: RIS item No.10 Business Risk 172
Table 142: RIS item No.11 Business Risk 173
Table 143: RIS item No.12 Business Risk 174
Table 144: RIS item No.13 Business Risk 175
Table 145: RIS item No.14 Business Risk 175
Table 146: RIS item No.15 Business Risk 176

Table 147: RIS item No.16 Business Risk 177
Table 148: RIS item No.17 Business Risk 178
Table 149: RIS item No.18 Business Risk 179
Table 150: RIS item No.19 Business Risk 179
Table 151: RIS item No.20 Business Risk 180
Table 152: RIS item No.21 Business Risk 181
Table 153: RIS item No.22 Business Risk 182
Table 154: RIS item No.23 Business Risk 183
Table 155: RIS item No.24 Business Risk 183
Table 156: RIS item No.25 Business Risk 184
Table 157: RIS item No.26 Business Risk 185
Table 158: RIS item No.27 Business Risk 186
Table 159: RIS item No.28 Business Risk 186
Table 160: RIS item No.29 Business Risk 187
Table 161: RIS item No.30 Business Risk 188
Table 162: RIS item No.31 Business Risk 189
Table 163: RIS item No.32 Business Risk 190
Table 164: RIS item No.33 Business Risk 190
Table 165: RIS item No.34 Business Risk 191
Table 166: RIS item No.35 Business Risk 192
Table 167: RIS item No.36 Business Risk 193
Table 168: RIS item No.37 Business Risk 193
Table 169: RIS item No.38 Business Risk 194
Table 170: RIS item No.39 Business Risk 195
Table 171: RIS item No.40 Business Risk 196
Table 172: RIS item No.41 Business Risk 196
Table 173: RIS item No.42 Business Risk 197
Table 174: RIS item No.43 Business Risk 198
Table 175: RIS item No.44 Business Risk 199
Table 176: RIS item No.45 Business Risk 199
Table 177: RIS item No.46 Business Risk 200
Table 178: RIS item No.47 Business Risk 201
Table 179: RIS item No.48 Business Risk 202
Table 180: RIS item No.49 Business Risk 202
Table 181: RIS item No.50 Business Risk 203

1. Overview

This section of the document serves as an introduction to the project proposal to complete the development portion of the said project. This section will also describe the purpose of the project and the objectives that are to be accomplished, the assumptions, the constraints that underlie the development of the project, and a summary of the project schedule and budget.

1.1 Project Summary

This section of the Software Project Management Plan (SPMP) provides a concise overview of the project, including its purposes, scope, and objectives. The summary also outlines the key assumptions and constraints that may impact the project, the expected deliverables, and a brief overview of the project's timeline and budget.

1.1.1 Purpose, Scope, and Objectives

The primary purpose of this study is to design, develop, and evaluate a web-based quotation and billing system for ExGen Battery Center & Car Wash. The system addresses the challenges of conventional customer inquiries, quotation preparation, and billing processes by providing an accessible digital platform where customers can check their vehicle needs, explore available services, browse products, and receive quotations and billing information. By organizing service, product, quotation, and billing information in one platform, the study seeks to improve the efficiency, accessibility, and organization of the business's customer service and transaction processes.

This study aims to design and develop a web-based quotation and billing system for ExGen Battery Center & Car Wash, allowing customers to check their vehicle needs, view available services and products, and obtain quotations and billing information based on their selected services and products while providing the business with an organized platform for managing quotations and billing transactions.

Specifically, this study aims to:

- To identify the functional requirements, available services, product catalog, customer check-up procedures, quotation processes, and billing procedures of ExGen Battery Center & Car Wash.
- To design and develop a web-based quotation and billing system featuring customer check-up, service viewing, product viewing, quotation generation, and billing functionalities.
- To evaluate the developed system in terms of functionality, reliability, usability, and performance using the ISO/IEC 25010 Software Quality Model and User Acceptance Testing (UAT).

1.1.2 Assumptions and Constraints

Assumption

The project is planned with the following assumptions for each stage of the development of the ExGen Battery Center and Car wash: Web-based Quotation & Billing System:

Requirements gathering

1. The team will conduct interviews with the owner and staff of Exgen Battery Center & Car Wash Between July 31, 2026 to September 2, 2026 gather detailed system requirements.
2. A questionnaire and transmittal letter will be prepared and approved before the interviews.
3. The owner and staff will provide accurate information regarding the current business workflow, service booking process, and quotation procedures, and will remain available for clarifications throughout the project.

System Design

1. All gathered requirements will be reviewed and validated before creating system diagrams, database design, and user interface mockups.
2. The team will use tools such as Draw.io for system diagrams, Figma for user interface design, and MySQL Workbench for database design.
3. Project decisions during this phase will be made collaboratively and in a timely manner to maintain the project schedule.

Development and Iteration

1. The team is expected to have the necessary technical skills in HTML, CSS, JavaScript, PHP, and MySQL to implement the proposed system.
2. Each sprint will focus on major modules such as the Customer Check-Up and Service Booking Module, Product and Service Module, Quotation and Billing Module, and Administrative Management Module.
3. Development tasks will be divided among members for both front-end and back-end implementation, with the prototype expected to be completed within the academic timeline.

Testing and Feedback

1. The owner, staff, and selected customers will participate in system testing to evaluate functionality, usability, reliability, and efficiency.
2. User feedback will be documented and incorporated into succeeding system improvements.
3. Testing will include verification of service booking, quotation generation, and data accuracy.

Deployment and Training

1. The system will be deployed on an affordable web hosting service with a MySQL database.
2. User manuals will be prepared, and system orientation and training will be provided to the owner and staff.
3. Final project documentation will be submitted to the instructor at the end of the semester.

Constraints

The project also has the following limitations in each stage of development:

Requirements Gathering

The owner and staff of ExGen Battery Center & Car Wash are the primary sources of information. However, their limited availability during scheduled interviews may delay the collection of requirements. Since the development team has little experience in conducting formal interviews, the information gathered may be incomplete or unclear. This means that who provides the data, when it is collected, what details may be missing, and how the process is conducted all affect the accuracy and completeness of the requirements.

System Design

The developer of the team will be responsible for producing diagrams, mockups, and database structures. Constraints arise because limited knowledge of certain design tools may slow down progress, and strict timeframes may force the team to simplify non-essential features. In this stage, who is affected are the developers, when delays occur is during design activities, what limitations exist are tool familiarity and time, and how these constraints manifest is through reduced design complexity.

Development and Iterations

The programmer and with the help of the team may face challenges in implementing advanced billing and quotation features due to limited technical expertise. Unexpected technical issues such as browser compatibility errors, database integration problems, or system failures may also occur, requiring additional debugging. Here, who is responsible are the developers, when problems arise is during sprint cycles and coding implementation, what issues may appear are technical errors and skill limitations, and how they are resolved is through debugging and adjustments that may extend the schedule.

Testing and Feedback

The owner, staff, and selected customers are expected to participate in evaluating the system. Their limited availability during the testing period, combined with the short academic timeline, reduces the extent of testing that can be performed. Feedback may also require revisions that extend the project timeline. In this stage, who participates are the users and stakeholders, when testing occurs is before deployment, what constraints exist are limited time and availability, and how feedback impacts the schedule is through revisions and adjustments.

Deployment and Training

The business owner and staff will rely on the available hardware, software, and internet connection to operate the system. Since the project must be completed within the academic semester, enhancements beyond the approved scope may not be possible. This shows who will use the system are the business staff, when deployment occurs at the end of the semester, what limitations exist are hardware, software, and internet dependency, and how the academic deadline restricts further improvements.

1.1.3 Project Deliverables

The following items listed in this subsection are the deliverables of the project.

1. **End Product (System)**
    - **Customer Quotation Module**
        - Customer information and vehicle check-up form
        - Vehicle information and requirements input
        - Service selection
        - Service booking and scheduling
        - Booking information recording and management
    - **Product and Service Module**
        - Product catalog for current available products
        - Service catalog for available services
        - Product and service details, including description and prices
        - Product and service management for authorized personnel
    - **Quotation and Billing Module**
        - Product and service selection for quotation
        - Calculation of the estimated or probable cost
        - Inclusion of possible additional expenses in the estimated cost
        - Generation of a quotation showing the probable amount
        - Recording of the final amount based on the final transaction
        - Comparison between the estimated amount and final amount
        - Generation of the final invoice or billing statement

- **Administrative Management Module**
    - Dashboard for viewing customer, quotation, and billing records
    - Customer information management
    - Service booking management
    - Quotation Management
    - Billing and transaction record management
    - Product and service management
    - Basic quotation and billing reports

2. **Project Documentation**
    - Software Project Management Plan (SPMP)
    - Software Requirements Specification (SRS)
    - Software Design Description (SDD)
    - Use Case Description and Diagram
    - Test Scripts and Test Results
    - Scrum Log (Agile development records)
    - User Documentation/Manual
3. **User Training**
    - Orientation for the business owner on how to use the system

1.1.4 Schedule and Budget Summary

This section shall provide a summary of the schedule and budget for the software project. The project's timeline shall be bounded by the months applicable to the students' school semester period.

Below is the schedule summary of the project:

Milestone	**Start Date**	**End Date**
Project Initiation	July 28, 2026	October 27, 2026
Project Management Plan	August 01, 2026	April 8, 2026
Requirements Analysis	July 06, 2026	October 27, 2026
Roles and Allocation	August 04, 2026	August 08, 2026
Sprint 1 Deliverable: Project Deliverables	November 16, 2026	December 16, 2026
Closure	April 1, 2026	April 08, 2026

Table 1: *Project Schedule Summary*

Below is the budget summary of the project. The full details of the project can be seen in section 5.

Resource	**Budget**
Printing and Documentation Materials (A4 bondpaper, ink, etc)	₱ 2,700
Mobile Data Load	₱ 100
Food	₱ 670
Total	₱ 3,470

Table 2: *Project Budget Summary*

1.2 Evolution of the plan

This document will be updated as the project progresses. Updates will be expected in the following sections:

Documents and Tasks	**Date**	**Description**	**Expected Outputs**
Requirements Gathering			
Creation and Distribution of Transmittal Letter	July 22 – July 31, 2026	Draft and send a formal request to conduct the study and schedule interviews with key stakeholders.	Approved and signed transmittal letter
Formulation of Interview Guide Questions	August 01 – August 14, 2026	Prepare and finalize structured interview questions tailored to extract user and system requirements.	Finalized interview questionnaire / guide
Client Interview	August 15 – August 21, 2026	Conduct structured interviews with the business owner, staff, and target users to gather detailed functional needs.	Interview notes, recordings, and gathered requirements
Requirements Assessment	August 15 – August 21, 2026	Analyze and compile gathered findings to establish system objectives, functional, and non-functional requirements.	Documented requirements specification list and prioritized objectives

System Architecture Design	August 22 – August 31, 2026	Define the structural model, behavior, data flows, and high-level architectural views of the system.	Context Diagram, Data Flow Diagram (DFD), Use Case Diagram, Sequence Diagram
Database Schema Design	August 22 – September 07, 2026	Structure the logical and visual layout of the relational database tables and attributes.	Entity Relationship Diagram (ERD) & Data Dictionary
User Interface Design	September 08 – October 31, 2026	Design user-centered wireframes and interactive prototypes for client and administrative interfaces.	UI/UX Mockups, Component Prototypes, and Screen Designs

***Table 3**: Evolution of the Plan*

2. Definitions

For the purpose of clarification, the important terms used in this document are defined as follows:

Agile Agile Methodology

- A software development methodology that follows an iterative process, allowing requirements and solutions to evolve through continuous collaboration between developers and clients. It promotes flexibility, adaptability, and the delivery of functional software in short development cycles called sprints.

Canva

- A web-based graphic design platform used to create visual content such as presentations, posters, infographics, social media graphics, and other design materials through customizable templates and design tools.

CSS Cascading Style Sheets

- A style sheet language used to define the appearance and layout of web pages written in HTML. It manages elements such as colors, fonts, spacing, and responsive design.

DFD Data Flow Diagram

- A visual model that illustrates how data flows within a system, showing the processes, inputs, outputs, and data storage involved.

ERD Entity-Relationship Diagram

- A diagram used to represent the entities in a database and the relationships between them, serving as a guide in database design.

Figma

- A web-based design and prototyping tool used to create user interfaces and collaborate on system designs in real time.

HTML Hypertext Markup Language

- The standard markup language used to create and organize the structure and content of web pages, including text, images, links, and other elements.

HW Hardware

- The physical components of a computer system, including devices such as the monitor, keyboard, motherboard, and storage drives.

JavaScript

- A programming language used to add interactive and dynamic features to websites, enhancing user experience and functionality.

Draw.io

- An online diagramming application used to create system diagrams such as flowcharts, Data Flow Diagrams (DFDs), Entity-Relationship Diagrams (ERDs), and other visual models.

Prototype

- A preliminary version of a system developed to demonstrate functionality, gather user feedback, and improve the design before the final implementation.

RDBMS Relational Database Management System

- A database management system that stores data in related tables and enables efficient organization, retrieval, and management of information.

Scrum Log

- A document used in Agile development to record sprint activities, completed tasks, project progress, and issues

encountered during development.

SDD Software Design Document

- A document that describes the overall design, architecture, and implementation details of a software system based on its requirements.

SPMP Software Project Management Plan

- A document that outlines how the software project will be planned, managed, monitored, and controlled throughout its development.

SRS Software Requirements Specification

- A document that defines the functional and non-functional requirements of the software system to serve as a guide during development.

SW Software

- A collection of programs, instructions, and data that enables a computer to perform specific tasks and functions.

UI User Interface

- The part of a software system that allows users to interact with it through elements such as forms, buttons, menus, and screens.

UML Unified Modeling Language

- A standardized visual language used to model, analyze, and document the design and structure of software systems.

VS Code Visual Studio Code

- A lightweight and versatile source code editor that supports programming, debugging, extensions, and version control for software development.

WBS Work Breakdown Structure

- A project management tool that organizes a project into smaller, manageable tasks and deliverables to simplify planning and execution.

3. Project Organization

This sub-clause of the documentation shall describe the assumptions on which the project is based and impose constraints on project factors such as the schedule, budget, resources, software to be reused, acquired software to be incorporated, technology to be employed, and product interfaces to other products.

3.1 External Structures (DIAGRAM)


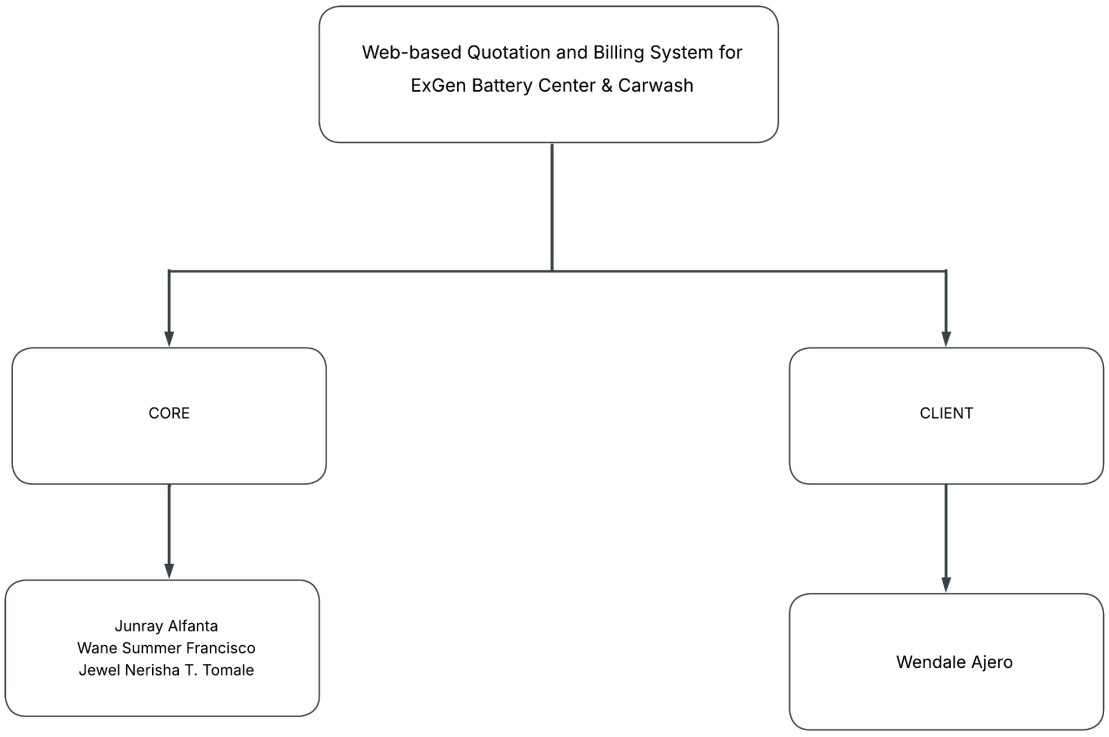


Figure 1: *External Structure*

The project is composed of two primary stakeholders: the research and development team and the client, Mr. Boyd Wendale Ajero. The research and development team consists of Junray T. Alfanta, Wane Summer J. Francisco, and Jewel Nerisha T. Tomale, who are responsible for the planning, analysis, design, development, testing, and documentation of the proposed ExGen Battery Center & Car Wash: Web-based Quotation & Billing System. Each member will contribute their knowledge and assigned responsibilities to ensure the successful completion of the project.

To ensure that the system meets the client's needs and expectations, the team will conduct regular meetings, consultations, and system demonstrations with Mr. Wendale Ajero throughout the development process. These interactions will allow the client to provide feedback regarding the system's features, functionality, usability, and alignment with the actual operations of the system. The team will use the feedback and recommendations provided by the client to make necessary improvements and refinements to the system. Through continuous collaboration between the research and development team and the client, the project will remain aligned with the business requirements and objectives while ensuring that the developed system is practical, functional, and suitable for its intended users.

3.2 Internal Structure (DIAGRAM)

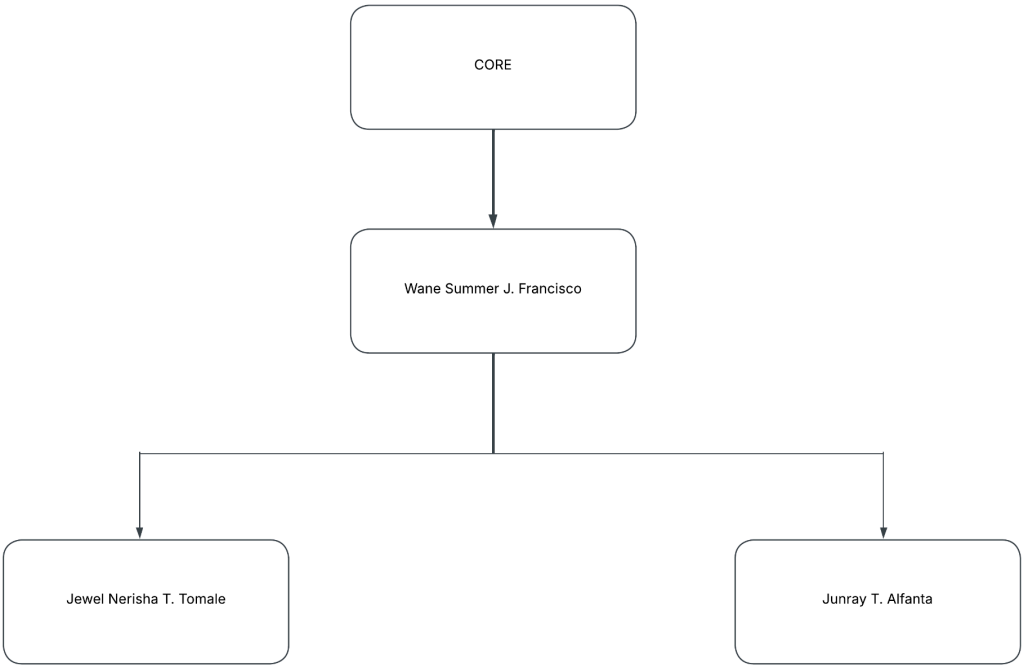

Within the Team, tasks are distributed among the members to ensure that each stage of the system development is properly addressed and completed efficiently. Wane Summer J. Francisco serves as the Project Lead, responsible for overseeing the overall progress of the project, coordinating schedules, managing team activities, and ensuring consistent communication with the client. Junray T. Alfanta is responsible for the System Design and Development, focusing on the design of the system interface, implementation of system features, and ensuring that the proposed system addresses the identified requirements. Jewel Nerisha T. Tomale takes charge of Quality Assurance and Documentation, responsible for testing the system, identifying issues, documenting project outputs, and ensuring that the developed system meets the required standards.

The internal workflow is organized around collaboration, with team members conducting regular meetings to monitor progress, discuss challenges, review their respective outputs, and coordinate necessary revisions before presenting the system to the client. This internal structure promotes clear responsibilities, effective teamwork, and an organized development process, ensuring that the project objectives are achieved and that the proposed ExGen Battery Center & Car Wash: Web-based Quotation & Billing System meets the needs of the client and its intended users.

3.3 Roles and Responsibilities

Project Organization Roles and Responsibilities:

Role	Person(s) Assigned	Responsibilities
Scrum Master/Team Leader	Wane Summer Francisco	o Software project planning and monitoring o Milestone and schedule planning and monitoring o Set and communicate the team meeting agendas. o Accountable for removing impediments to the ability of the team to deliver the product goals and deliverables.
Business Analyst	Junray Alfanta	o Collect and Interpret client requirements. o Works with the team to ensure the system

Role	Person(s) Assigned	Responsibilities
		follows the requirements. o Updates documentations as per changes requested by the client.
Technical Developer	Junray Alfanta	o Codes and builds the system, realizing the system design. o Adheres the functional and non-functional requirements of the system. o Manages the database and backend functions o Use Git as the version control and tracker to ensure proper development tracking.
System Designer	Junray Alfanta	o Designs the layout, interface, and structure of the system o Create prototypes, diagrams, and models to guide development. o Ensures the design is user-friendly and accounts for user-experience.

Role	Person(s) Assigned	Responsibilities
Budget Manager	Wane Summer Francisco	o Ensures the team spending is inline and follows the planned budget o Make sure resources are properly and efficiently used
Process Manager	Junray Alfanta	o Confirms if the team is following the development process. o Reviews if methods and standards are applied correctly.
Quality Assurance (QA) Lead	Jewel Nerisha Tomale	o Inspects the quality of outputs, including the documents and system features. o Initiates testing and proof-reading activities to pin-point issues o Ensures the system meets requirements before release.
Documentation Officer	Jewel Nerisha Tomale	o Records meeting notes during conversations with the client. o Progress documentation updates to ensure the team is working and on schedule o Store all reports and files in a Google Drive for easy access.

Role	Person(s) Assigned	Responsibilities
Scheduler / Time Manager	Jewel Nerisha Tomale	○ Keep track of deadlines and milestones. Updates the project timeline in Google Docs. Reminds members of their tasks and follow-up on progress.

Table 4: *Roles and Responsibilities*

4. Managerial Process Plans

This clause of the SPMP shall specify the project management processes. This clause shall be consistent with the statement of project scope and shall include the project start-up plan, risk management plan, project work plan, project control plan, and project closeout plan.

4.1 Start-Up Plan

This section outlines the initial processes and strategies needed to set a strong foundation for ExGen Battery Center & Car Wash. This will include estimations, staffing, resource acquisition, and training plans. The project officially began July 31, 2026 and is in route for completion in April 2027. The development team will begin with detailed coordination with the client, Mr. Wendale Ajero, to confirm the project's objectives, features, design, and the expected deliverables. This direct collaboration ensures that the project aligns with both academic requirements and business's practical needs.

4.1.1 Estimation Plan

This section outlines the practices and strategies used by the project team to estimate the time, cost, and resources required for the successful completion of the ExGen Battery Center & Car Wash: Web-Based Quotation & Billing System.

Component	**Details**
Discussing Project Details with the Client	o The project team and the client (owner of ExGen Battery Center & Car Wash) will align on the project's goals, scope, operational workflow, and deliverables. o A project timeline will be prepared using a Gantt chart, showing the breakdown of tasks and sprints for the semester.
Collecting and Reviewing Requirements	o Requirements will be gathered through interviews, site observations, and questionnaires with the owner and staff. o These requirements will guide the Work Breakdown Structure (WBS) and form the basis for estimating the time needed for each module: Customer Check-Up and Service Booking Module, Product and Service Module, Quotation and Billing Module, and Administrative Management Module.
Planning Budget, Manpower, and Resources	o Each team member will be assigned specific roles. o Resources include personal laptops, internet connection, and development tools such as VS Code, PHP, MySQL, HTML/CSS/JavaScript, Figma, and Draw.io. o The project has minimal direct financial cost, limited primarily

	to printing, document binding, internet usage, and optional domain/hosting deployment needs.
Learning Required Tools and Methods	o Team members will familiarize themselves with PHP-MySQL integration, quotation generation logic, and Agile Scrum practices. o Training will be informal, conducted through self-study, developer documentation, and peer mentoring.

Table 4: *Estimation Plan*

4.1.2 Staffing Plan

The team has fixed staffs that were based on initial estimates. The project will require the human resources shown in the table below:

Human Resource Type	Personnel	Weekly Hours	Quantity
Team Leader/ Project Manager	Wane Summer Francisco	17 Hours	1
Technical Developer		20 Hours	1
Business Analyst		4 Hours	1
System Designer		10 Hours	1
Budget Manager		5 Hours	1
Process Manager		5 Hours	1
Quality Assurance (QA) Lead	Jewel Nerisha Tomale	5 Hours	1
Scheduler / Time Manager	Jewel Nerisha Tomale	5 Hours	1
Documentation Officer	Jewel Nerisha Tomale	10 Hours	1

Table 5: *Staffing Plan*

4.1.3 Resource Acquisition Plan

This section details the plan for acquiring and maintaining the necessary resources, this will include the hardware, development and design softwares, budget, and skills.

- **Hardware Resources**

  Each team member will use their personal laptops with their own internet connections, this will serve as the workstation for development, design, and documentation.

- **Software Resources**

  Free tools will be used for the project, including code IDEs, database, design, and documentation tools. These already exist on the researcher's personal computers before the start of the project and will be updated when needed.

Resource Category	**Required Resource**	**Purpose**	**Acquisition Method**	**Person Responsible**
Software	Visual Studio Code	Source code development	Microsoft. (2021, November 3). *Visual studio code*. Microsoft. Code. https://code.visualstudio.com/download?_ex	Junray Alfanta

			p_download=d53503e735	
Software	GitHub	Version control and source code repository	Create a GitHub organization/repository and provide access to all team members.	Jewel Nerisha Tomale
Software	Google Chrome / Mozilla Firefox	Testing and debugging the web application	https://www.pgadmin.org/download/pgadmin-4-windows/	Wane Summer Francisco
Software	Figma	UI/UX design and prototyping	https://www.figma.com/downloads/	Wane Summer Francisco
Collaboration Tool	Microsoft Teams / Google Meet	Team meetings and client consultations	https://meet.google.com/home	Jewel Nerisha Tomale
Collaboration Tool	Google Drive	Document sharing and backup	https://drive.google.com/home	Jewel Nerisha Tomale
Hardware	Laptop/Desktop Computer	Software development, testing, and documentatio	Team members will use their personal laptops or university laboratory computers	All Team Members

		n	when needed.	
Hardware	Internet Connection	Online collaboration, research, and deployment	Team members will use personal internet connections or university Wi-Fi.	All Team Members
Facilities	Computer Laboratory	Development meetings and system testing	Reserve the laboratory through the department when required.	Jewel Nerisha Tomale
Human Resource	Client Representativ e	Requirement gathering, validation, and user acceptance testing	Coordinate with the partner organization and schedule meetings through formal communication.	January Alfanta
Human Resource	Project Adviser	Technical guidance and project evaluation	Schedule regular consultation meetings during the project duration.	Entire Team
Funding	Printing and Documentatio n Budget	Printing reports, user manuals, and presentation materials	Team members will equally contribute to the required project expenses.	All member
Cloud Hosting	Render, Vercel, or	Deployment of the web	Register for a free account initially and	Wane Summer

	Firebase	application	upgrade only if additional features are required.	Francisco
Database	MySQL / Firebase Firestore	Data storage and management	Install MySQL locally or create a free cloud database account before implementation.	Junray Alfanta

Table 6 : *Source Catalog Details*

4.1.4 Project Staff Training Plan

Resource Category	Required Resource	Purpose	Acquisition Method	Person Responsible
Software	Visual Studio Code	Front-end and Backend System Development	Microsoft. (2021, November 3). *Visual studio code*. Microsoft. Code. https://code.visualstudio.com/download?_exp_download=d53503e735	Junray Alfanta
Software	GitHub	Version control and source code repository	GitHub. (2025). GitHub. GitHub. https://github.com/	Wane Summer Francisco

Software	PostgreSQL & pgAdmin 4	Local server and database management	https://www.postgresql.org/download/ & https://www.pgadmin.org/download/pgadmin-4-windows/	Jewel Nerisha Tomale
Software	Figma	UI/UX design and prototyping	https://www.figma.com/downloads/	Wane Summer Francisco
Collaborative Tool	Draw.io	Create Diagrams and Cases	app.diagrams.net	Junray Alfanta
Collaboration Tool	Google Meet	Team meetings and client consultations	https://meet.google.com/home	Jewel Nerihs Tomale
Collaboration Tool	Google Drive and Docs	Document sharing	https://drive.google.com/home	Jewel Nerisha Tomale
Hardware	Laptop	Software development,	Each team members have a personal device	All Team Members

		testing, and documentation	to work on the software project	
Collaborative Tool	MyBib	Create Reference APA 7th Edition Citations on cited links	mybib.com	All Team Members

Table 7: *Project Staff Training Plan*

4.2 Work Plan

This clause of the SPMP shall specify the work activities, schedule, resources, and budget details for the software project.

4.2.1 Work Activities

The following table shows our work activities for this project.

Task	Start Date	End Date
Preparation of Transmittal Letter	July 20, 2026	July 30, 2026
Formulation of Interview Questions	August 7, 2026	August 17, 2026
Client Interview & Data Gathering	August 17, 2026	August 21, 2026
Requirements Analysis & Documentation	August 21, 2026	August 24, 2026
System Design - Context Diagram	August 25, 2026	August 26, 2026
System Design - Data Flow Diagram (DFD)	August 26, 2026	August 28, 2026
System Design - Use Case & Activity Diagram	August 28, 2026	September 09, 2026
User Interface Mockups (Figma)	September 10, 2026	October 27, 2026
Development – Customer Check-Up and Service Booking Module		
Development – Product and Service Module	November 24, 2026	November 30, 2026
Development – Quotation Generation Module	December 1, 2026	December 9, 2026
Development – Administrative Management Module	December 10, 2026	December 16, 2026

Integration of System Modules	January 4, 2027	January 6, 2027
User Testing with Client and Staff	January 7, 2027	January 9, 2027
Feedback Collection and Analysis	January 14, 2027	January 16, 2027
User Feedback Implementation	January 17, 2027	January 21, 2027
System Refinement and Bug Fixing	January 22, 2027	February 3, 2027
Deployment and User Training	February 7, 2027	February 15, 2027
Final Documentation and Submission	February 25, 2027	April 7, 2027

Table 8: *Work Activities*

4.2.2 Schedule Allocation

The overall time frame of the project is constrained to two semesters, starting in the last week of June 2026 until first week April 2027.

4.2.3 Resource and Budget Allocation

Below is the provided itemization of the resources allocated to their respective budget in the project work breakdown structure.

Resource	**Budget**
Documentation Printing & Binding	1,000 PHP
Web server	1,200 PHP
Database	360 PHP
Web Domain	0 PHP
Team Member's Expenses	N/A
Petty Cash	500

Table 9 : *Resource and Budget Allocation*

4.3 Control Plan

This section of the SPMP shall specify the metrics, reporting mechanisms, and control procedures necessary to measure, report, and control the product requirements, the project schedule, budget, resources, and the quality of work processes and work products. All elements of the control plan should be consistent with the organization's standards, policies, and procedures for project control as well as with any contractual agreements for project control.

4.3.1 Requirements Control Plan

This section ensures that all stakeholder, business, and functional requirements for the ExGen Web-Based Quotation and Billing System are systematically captured, analyzed, managed, and addressed throughout the project lifecycle.

Area	**Plan / Approach**
Requirements	The owner and staff of ExGen Battery Center & Car Wash are the primary stakeholders who provide the necessary information. Requirements will be gathered between July 06, 2026 and October 27, 2026 through structured interviews, direct observation, and questionnaires. What will be collected are both functional and non-functional requirements, including customer check-up, service booking, product and service viewing, quotation preparation, probable cost calculation, billing, and administrative record management. How this will be achieved is by documenting all findings in the Software Requirements Specification (SRS), which will serve as the foundation for design and development.
Design	The team will translate the gathered requirements into system architecture, database structures, and user interface designs. This will occur after requirements finalization, using tools such as MySQL Workbench for database design and Figma for UI mockups. What will be designed are diagrams including the System Context Diagram, Data Flow Diagrams (DFD), Use Case Diagrams, and Activity Diagrams. How this will be achieved is by modeling workflows for customer check-up, service booking, product and service viewing, quotation generation, billing, and administrative management.

Implementation	The team will build the system through sprint iterations. This will take place from November 2026 until early 2027, with each sprint focusing on a specific module. What will be implemented are the customer check-up and service booking module, product and service module, quotation and billing module, and administrative management module. How this will be achieved is by coding with HTML, CSS, JavaScript, PHP, and MySQL, then integrating all modules into one complete web-based application.
Testing	The team, owner, staff, and selected customers will participate in system evaluation. This will occur after the completion of major modules, prior to deployment. What will be tested are system functionality, reliability, usability, and performance, including customer check-up, service booking, product and service selection, quotation generation, billing, and record management. How this will be achieved is through User Acceptance Testing (UAT) and evaluation against the ISO/IEC 25010 Software Quality Model, with feedback documented and addressed through bug fixing and refinements.
Deployment	the verified system will be released to an affordable web hosting environment with a MySQL database. This will occur after successful testing and approval. What will be deployed is the complete web-based quotation and billing system, prepared for actual business use. How deployment will be achieved is by providing orientation and training to the owner and staff, covering customer and vehicle information management, service booking, product and service management, quotation generation, billing procedures, and administrative record management.

Maintenance	The team will monitor the system and address minor errors, technical issues, and refinements based on user feedback. This will occur after deployment and continue until the project closure on April 7, 2027. What will be maintained are backups, documentation, and system records. How this will be achieved is by applying updates, resolving issues, and finalizing project outputs for submission and presentation.

Table 10 : *Requirements Control Plan*

4.3.2 Schedule Control Plan

To make sure the project stays on track, the team will regularly monitor progress and compare it with the planned schedule. The following plan will be used:

AREA	**Plan / Approach**
Schedule Monitoring	We will use a Gantt chart and sprint schedule to keep track of our tasks. This will help us see if we are following the timeline or if we are behind.
Progress Review	Our team will meet every Sunday to check what we finished last week and plan what we need to do next. We will also show progress to the client during important milestones.
Handling Delays	If some tasks are not finished on time, we will move them to the next sprint. The team will make sure to complete both the delayed tasks and the new ones.
Responsibility	The Project Manager will handle the schedule, but each member must give updates about their assigned tasks during meetings.
Control Tools & Techniques	We will use Gantt charts, task checklists, and progress reports to monitor deadlines and progress. We will also follow Agile Scrum practices to adjust our sprints when needed.
Change Management	If there are big delays or changes, the schedule will be updated after talking with the client and instructor. Any changes will be written down and shared with the team.

Table 11 : *Schedule Control Plan*

4.3.3 Budget Control Plan

To make sure project expenses stay within the planned budget, the team will regularly track and review financial spending. The plan is as follows:

Key Area	Plan / Approach
Budget Monitoring	Actual project expenses will be compared with the planned budget using financial records and expense trackers maintained by the — Wane Summer Francisco
Review Process	At the end of each sprint, the team will conduct a budget review before starting the next sprint. Wane Summer Francisco will lead the review, while Jewel Nerisha Tomale will provide updates on development-related expenses and Junray Alfanta will report on documentation and other project-related costs.
Handling Variances	If actual expenses are higher or lower than the planned budget, the Summer Wane Francisco will analyze the difference and make necessary adjustments. Jewel Nerisha Tomale and Junray alfanta will suggest cost-saving measures for their respective areas.
Responsibility	Wane Summer Francisco, the Budget Manager is responsible for the overall project budget. Junray Alfanta will monitor expenses related to system development and technical tools, while Jewel Nerisha Tomalel will track expenses related to documentation and other assigned activities.

Control Tools & Techniques	Budget records, expense reports, and simple spreadsheets will be used to track project expenses and monitor the use of available resources.
Change Management	For major budget changes, Wane Summer Francisco will consult with the client and instructor. All approved changes will be documented by Jewel Nerisha Tomale and shared with the team to ensure transparency.

***Table 12** : Budget Control Plan*

4.3.4 Quality Control Plan

This section outlines the quality control plan, detailing how testing will be conducted, feedback gathered, and performance standards ensured to maintain and improve the website's quality.

Key Area	**Plan / Approach**
Testers	Jewel Nerisha Tomale, the Quality Assurance (QA) Lead will oversee the overall testing process and check the quality of the system. Junray Alfanta ,the Technical Developer will conduct technical testing, including unit and integration testing. Wane Summer Francisco, the System Designer will test the user interface and user experience for usability and consistency. Selected staff from ExGen Battery Center & Car Wash will also participate in User Acceptance Testing (UAT).
Testing Methods & Parameters	Unit testing will be handled by Wane Summer Francisco. Integration and system testing will be conducted jointly by Wane Summer and Jewel Nerisha Tomale. User Acceptance Testing (UAT) will be coordinated by Jewel Nerisha Toamlewith the owner, staff, and selected customers of ExGen Battery Center & Car Wash.
Feedback & Documentation	Junray Alfanta will collect feedback through surveys, interviews, and direct observation during UAT. Jewel Nerisha Tomale will record technical errors and handle bug fixes, while Wane Summer Francisco will document issues related to the user interface and design. Testing results and reports will be stored in the team's project repository using Google Drive

Performance Standards	The system must meet the required standards, including accurate service booking, quotation generation, probable cost calculation, correct billing processes, reliable functions, fast response times, and an easy-to-use interface.

4.3.5 Reporting Plan

This subsection of the SPMP outlines the reporting mechanism that is in place. There are internal and external reporting mechanisms.

4.3.5.1 Internal Reporting Plan

These reports are intended for the project team to maintain coordination, monitor development progress, track issues, and ensure that project activities remain aligned with the approved schedule.

Report Type	Information Gathered By	Prepared By	For Whom (Audience)	Tools Used
Team Availability Report	Team Members	Project Manager	Project Team	Google Sheets for attendance logs; Messenger for availability updates
Project Status Report	Development Team	Project Manager	Project Team & Adviser	Google Docs for documentation; Messenger/Email for sharing
Project Health Report	QA/Testing Team	Quality Assurance Lead	Project Manager, & Project Team	Google Sheets for QA logs; Google Docs for reporting
Time Tracking Report	Individual Team Members	Scrum Master / Project Manager	Project Manager & Project Team	Google Sheets for time logs

Table 13 : *Internal Reporting Plan*

4.3.6 Metrics Collection Plan

This section outlines the key metrics used to measure the success of the project, how data is collected and how results are analyzed and acted upon.

Week	Planned Tasks	Completed Tasks	Unfinished Tasks	Completion Rate (%)	Remarks
Week 1					
Week 2					

Table 14 : *Weekly Objectives Metrics*

This metric measures the team's progress by comparing planned tasks with completed and unfinished tasks.

Week	Meetings Held	Issues Raised	Resolved Rate (%)	Remarks
Week 1				
Week 2				

Table 15 : *Team Collaboration Metrics*

This metric checks how well the team works together through weekly meetings and member evaluations. It helps see who needs support and who is contributing well to the project.

Iteration	Planned Cost (php)	Actual Cost (php)	Variance (php)	Variance (%)	Remarks
Iteration 1					
Iteration 2					

Table 16 : *Budget Metrics*

This metric helps the Budget Manager check if the team’s actual spending matches the planned budget for each iteration, making it easier to monitor financial

performance.

Iteration	Consultation Date	Instructor Consulted	Key Comments	Action Taken
Iteration 1				
Iteration 2				

Table 17 : *Client Feedback Score Metrics*

This metric uses feedback from another instructor to check the project's clarity, quality, and effectiveness.

Iteration	Test Type	Passed	Failed	Remarks
Iteration 1				
Iteration 2				

Table 18 : *Quality Assurance Metrics*

This metric checks how each module or feature works during testing and helps the team decide what to fix first before deployment.

Risk ID	Risk Name	Description	Priority

Table 19 : *RMMM Traceability Metrics*

This metric helps the Risk Manager review each risk, check how likely it is to happen, and see its possible effect on the project, including project, technical, and business risks.

4.4 Risk Management Plan

This section presents the Risk Management Plan for the ExGen Battery Center & Car Wash: Web-based Quotation & Billing System. It identifies the potential risks that may affect the project and provides appropriate mitigation, monitoring, and management strategies. The risks are classified into project risks, technical risks, and business risks. The complete RMMM Traceability Matrix and Risk Information Sheets are presented in Appendix C.

4.5 Closeout Plan

The proposed project will be closed by the end of October 29, 2026. The project team must comply with the required 70% of the total project's requirements to ensure all deliverables are met. A final review of change request, project documentation, source code and other related materials will be conducted to confirm all commitments have been completed. But the development of the project for unforeseen errors or new features will continue. All necessary documentation must be printed and presented to the client. The client will also be presented with the project closure approval page, and their signatures are required to confirm that they are satisfied with the project output.

5. Technical Process Plan

This clause of the SPMP shall specify the development process model, the technical methods, tools, and techniques to be used to develop the various work products, plans for establishing and maintaining the project infrastructure, and the product acceptance plan.

5.1 Process Model

The project will use the Agile Process Model. Development will proceed through a series of short and iterative sprints from 2026 until April 7, 2027, which is the target date for the completion of the final system. The detailed schedule of activities is provided in Section 4.2.1 Work Activities.

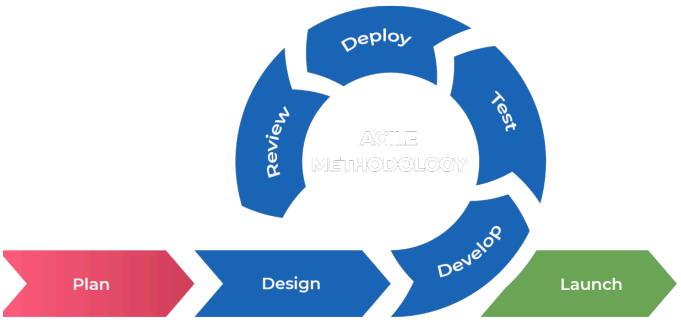


Figure 2: *The Agile Methodology*

Agile was selected because it is suitable for a project that requires regular client involvement, continuous improvement and development, and flexibility in handling new or changing requirements. The ExGen Battery Center & Car Wash Web-based Quotation and Billing System involves real business processes such as managing products and services, handling customer check-ups and service bookings, generating quotations with probable costs, and managing billing and transaction information. These processes may change or require refinement as development progresses.

Using Agile allows the team to:

- Deliver system features in small, working portions;
- Gather feedback early and regularly from the client;
- Adjust quickly to new or changing requirements; and
- Maintain continuous communication and collaboration among team members.

This makes Agile suitable for developing the ExGen Battery Center & Car Wash Web-Based Quotation and Billing System because the project involves actual business processes such as customer check-ups, service booking, product and service selection, quotation generation, probable cost calculation, billing, and administrative record management. These processes may require refinement as development progresses.

Agile Methodology Phases

1. Requirements Phase

From July 06, 2026 to October 27, 2026, the team will gather and analyze detailed requirements by conducting interviews, observations, and questionnaires with the owner and staff of ExGen Battery Center & Car Wash. The focus will include the customer check-up process, service booking procedures, available products and services, quotation preparation, probable cost calculation, billing procedures, and administrative record management. Tools such as Google Docs, meeting notes, and other documentation tools will be used to record and organize the gathered information. The main deliverable of this phase is the Software Requirements Specification (SRS), which will serve as the basis for the succeeding system design and development activities.

2. Design Phase

The design phase will translate the gathered requirements into system architecture, database structures, and user interface designs. The team will develop the System Context Diagram, Data Flow Diagrams (DFD), Use Case and Activity Diagrams, and other necessary system models to establish the flow of data and user interactions. The database structure will be designed using MySQL Workbench, while user interface mockups and prototypes will be created using Figma. The designs will focus on the customer check-up and service booking interface, product and service viewing, quotation and billing processes, and administrative management interface.

3. **Implementation Phase**

Development will be carried out through focused sprint iterations using HTML, CSS, JavaScript, PHP, and MySQL:

- Sprint 1 (Customer and Service Booking): Development of the customer check-up form and service booking features, including customer, vehicle, and booking information.
- Sprint 2 (Product and Service): Development of the product and service viewing features and management of available products and services.
- Sprint 3 (Quotation and Billing): Development of quotation generation, probable cost calculation, additional expense consideration, final amount recording, and billing functions.
- Sprint 4 (Administrative Management): Development of the administrative dashboard for managing customer records, service bookings, quotations, billing transactions, products, and services.
- Module Integration: Integration of the developed modules, database, and system functions into one complete web-based application.

4. **Testing Phase**

The system will undergo functional, technical, and user testing after the implementation of the major modules. The development team, owner, staff, and selected customers of ExGen Battery Center & Car Wash will participate in testing and User Acceptance Testing (UAT). Testing will evaluate the system's functionality, reliability, usability, and performance based on the ISO/IEC 25010 Software Quality Model. Test scenarios will include customer check-up, service booking, product and service selection, quotation generation, probable cost calculation, billing, record management, and data accuracy. Feedback and identified issues will be documented and addressed through bug fixing and system refinement.

5. Deployment Phase

After testing and approval, the verified system will be deployed to an affordable web hosting environment with a MySQL database. The team will prepare the system for actual use and provide orientation and training to the owner and staff of ExGen Battery Center & Car Wash. Training will cover customer and vehicle information management, service booking, product and service management, quotation generation, billing procedures, and administrative record management. The necessary user documentation will also be provided to support proper system use.

6. Maintenance Phase

Following deployment, the team will monitor the system and address minor errors, technical issues, and necessary refinements based on user feedback. The team will also finalize the required project documentation, maintain backups and system records, and prepare the final project outputs for submission and presentation. The project will be formally closed on April 7, 2027, subject to the completion and acceptance requirements stated in the SPMP.

5.2 Methods, Tools, and Techniques

The methods and techniques listed in this table will be evaluated and applied in specific areas of the project as appropriate:

Category	**Tools**
Requirements Gathering	Interview Guide Questions, Google Docs, Client Interviews, Transmittal Letters
System Design	Figma for UI/UX Wireframing and Mockups, Draw.io for Context Diagram, DFD, ERD, Use Case, Activity, Sequence, Class, Component, and Communication Diagrams
Operating System	Windows 10/11 for local development and testing, Android/iOS devices for responsive interface testing
Programming Languages	HTML5, CSS3, JavaScript, PHP, SQL
Development Tools	Visual Studio Code, MySQL Workbench, Git, GitHub
Source Code Control	MySQL and MySQL Workbench
Testing Methods	Black-Box Functional Testing, Unit Testing, Integration Testing, User Acceptance Testing (UAT), ISO/IEC 25010 Quality Evaluation
Testing Tools	Google Chrome Developer Tools, browser testing tools, test case documents
Documentation Tools	Google Docs, Google Drive, Microsoft Word
Communication & Collaboration	Google Meet (Virtual Adviser Consultation), Gmail (Official Transmittals), Messenger Group Chat (Team Coordination & Client Updates)
Project Management	Gantt Chart, Scrum Log, Google Sheets

***Table 20**: Methods, Tools, and Technique*

5.3 Infrastructure Plan

The system will be developed and deployed using affordable and reliable infrastructure suitable for the needs of ExGen Battery Center & Car Wash. Since the system is web-based, the development team will use personal computers and available internet connections for development, testing, documentation, and deployment. The final system will use a web hosting service with a MySQL database for storing and managing customer, service booking, quotation, and billing information.

Component	Specification / Description
Development Workstations	Personal laptops or desktop computers used by team members for system development, database management, testing, and documentation
Hosting Server	Affordable cloud-based web hosting service for deploying the completed ExGen Web-Based Quotation and Billing System
Database Server	MySQL database for storing customer, vehicle, service booking, product, service, quotation, and billing records
Database Management	MySQL Workbench for database creation, management, testing, and maintenance
Internet Connection	Personal internet connections or university Wi-Fi for development, collaboration, research, testing, and deployment
Client Access Devices	Desktop computers, laptops, tablets, or smartphones with a modern web browser for accessing the system
Browser Environment	Google Chrome and Mozilla Firefox for system access, testing, and debugging
Source Code Repository	GitHub for source-code storage, version control, branch management, and backup
Project Documentation Storage	Google Drive for storing SPMP, SRS, SDD, reports, testing documents, and other project files
Monitoring and Support	Browser developer tools, GitHub repository, Google Drive, and database backups for monitoring, troubleshooting, and recovery

Table 21: *Infrastructure Plan*

5.4 Product Acceptance Plan

The Product Acceptance Plan for the ExGen Battery Center & Car Wash project explains how the system and its deliverables will be reviewed and accepted by the client. Acceptance will be based on functionality, reliability, usability, performance, and compliance with the approved requirements. The client will participate in demonstrations, inspections, testing, and User Acceptance Testing (UAT). Identified issues will be documented and corrected before final approval. Final acceptance will be confirmed through the project closure approval page signed by the client. This follows the same acceptance approach used in the reference SPMP.

Work Products

The project documentation will be reviewed by the development team, project adviser, and client where applicable. Documents must be complete, properly formatted, consistent with approved requirements, and free from major errors before approval.

The work products include:

- Software Project Management Plan (SPMP)
- Software Requirements Specification (SRS)
- Software Design Description (SDD)
- Use Case Description and Diagram
- Test Scripts and Test Results
- Scrum Log
- User Documentation/Manual
- Project Monitoring Reports
- Feedback Reports
- Source Code
- Final System Version

Project Deliverables

The following deliverables will be reviewed and demonstrated to the client:

Customer Check-Up and Service Booking Module

- Customer and vehicle information
- Service selection
- Service booking and scheduling
- Booking information recording and management

Product and Service Module

- Product catalog
- Service catalog
- Product and service descriptions and prices
- Product and service management

Quotation and Billing Module

- Product and service selection
- Estimated/probable cost calculation
- Additional expense consideration
- Quotation generation
- Final amount recording
- Estimated versus final amount comparison
- Final billing statement or receipt

Administrative Management Module

- Customer records
- Service booking records
- Quotation records
- Billing and transaction records
- Product and service management
- Basic reports

The system will be accepted when the major functions operate according to the approved requirements, required test cases are completed, critical issues have been resolved, and the client confirms that the system meets the business requirements.

The approval signatures from the company president and other representatives are required to confirm consent to and validity of the above acceptance plan. A copy of the signed approval form will be attached to the thesis documentation's appendices.

6. Supporting Process Plans

This section of the SPMP describes the processes that coordinate the development and life cycle of the activities contained in the main processes, i.e. organizational and business processes. These processes can be undoubtedly cross processes, so that they contribute to the achievement of objectives between different areas of the project

6.1 Documentation Plan

The Documentation Plan defines how project documentation will be prepared, reviewed, stored, and distributed. Team members will prepare the documents, while the Project Manager, project adviser, and client will review them as applicable. The structure below follows the reference document's Document–Description–Due Date–Distribution format.

The table headings are defined as follows:

Document	**Description**	**Due Date**	**Distribution list**
Software Project Management Plan (SPMP)	Defines the project management plan.	August 2026	Document repository, team members, project adviser
Software Requirements Specification (SRS)	Defines the functionality that is required by the customer.	October, 2026	Document repository, team members, project adviser, client
Use Case Description and Diagram	A written description of how users will perform tasks on your website.	October 2026	Document repository, team members, project adviser, client

Software Design Description (SDD)	A written description of a software product, that a software designer writes in order to give a software development team overall guidance to the architecture of the software project.	October 2026	Document repository, team members, project adviser, client
Test Scripts and Test Results	Tests that are to be executed and their respective results.	December 2026	Team members, project adviser
Scrum Log	The log of the whole process.	April 2027	Team members, project adviser
User documentation	The documentation for the end-user of the website.	April 2027	End-users, client, project adviser
Developer documentation	The documentation for the instructions on how to integrate the project's library to their own web apps.	April 2027	Development team, project adviser
Final Project Report & Acceptance Form	Consolidates all documents, reports, and signed approval forms.	April 2027	Client, project adviser, college faculty

Table 22: *Documentation Plan*

6.2 Configuration Management Plan

The Configuration Management Plan ensures that all project files, source code, database files, and documents for the ExGen Battery Center & Car Wash: Web-Based Quotation & Billing System are properly organized, tracked, and updated throughout the development process. This helps prevent confusion, loss of work, and inconsistencies and ensures that the team is always working with the latest approved version of the project deliverables.

Key Area	Plan / Approach
Purpose	To ensure that all project files, source code, diagrams, documents, and test cases are properly managed, organized, and documented throughout the development process.
Configuration Manager	The Project Manager will oversee configuration management activities and ensure that approved project baselines are maintained.
Scope	Covers source code, database files, UI designs, diagrams, SPMP, SRS, SDD, test documents, reports, and final system versions.
Version Control	GitHub will be used for source code and version tracking. Google Drive will be used for project documents and backups.
Change Management	Any requested change will follow the process: request → review → impact analysis → approval → implementation → documentation update.
Auditing & Reporting	Regular reviews will verify that files and system components remain consistent with approved requirements.

Table 23: *Configuration Management Plan*

6.3 Verification and Validation Plan

The Verification and Validation Plan defines how the team will verify that the system is being developed correctly and validate that it satisfies the actual needs of ExGen Battery Center & Car Wash.

ISO/IEC 25010 Quality Characteristic	Verification Approach (Are we building the product right?)	Validation Approach (Are we building the right product?)
Functionality (Suitability, Accuracy, Compliance)	Perform requirements traceability, code reviews, and functional testing of customer check-up, service booking, quotation, billing, and administrative functions.	Conduct User Acceptance Testing (UAT) with the owner and staff to confirm that the system supports actual ExGen business processes.
Performance Efficiency	Test page loading, quotation calculation, billing processing, and database response times.	Ask users to perform common system tasks and evaluate whether the system responds within an acceptable time.
Usability (Understandability, Learnability, Operability)	Review interface layouts, navigation, forms, labels, and system workflows.	Conduct user testing with the owner, staff, and selected users to determine whether the system is easy to understand and use.

Reliability	Perform repeated tests and error handling checks for quotation, booking, billing, and record management.	Observe system behavior during actual user testing and confirm that important transactions are completed without major errors.
Security (Confidentiality, Integrity, Authenticity)	Review authentication, access control, validation, and protection of customer and transaction information.	Verify with authorized users that sensitive administrative functions are accessible only to intended personnel.
Maintainability (Changeability, Stability, Testability)	Conduct code reviews and check source-code organization, database structure, and system components.	Validate that common updates such as product prices, service information, and quotation/billing records can be performed without affecting other functions.
Compatibility (Adaptability, Installability, Conformance)	Test the web application using supported browsers and different screen sizes.	Have selected users access the system through available devices to confirm consistent behavior.

Table 24: *Verification and Validation Plan*

6.4 Quality Assurance Plan

This section will describe the plans for assuring that the quality of delivered work products is consistent with what is expected for the project.

Key Area	Plan/Approach
Purpose	Ensure that all project deliverables, system modules, documentation, and testing outputs meet the approved project requirements and quality standards.
Scope	Covers the Customer Check-Up and Service Booking Module, Product and Service Module, Quotation and Billing Module, Administrative Management Module, source code, database, documentation, diagrams, and test cases.
Quality Analyst	Jewel Nerisha Tomale will oversee QA activities, testing records, issue tracking, and quality verification.
Technical Testing	Junray Alfanta will conduct technical testing, including unit and integration

	testing.
UI/UX Review	Wane Summer Francisco will review interface usability, consistency, and user experience.
RMMM Alignment	Quality issues will be reviewed against the risks identified in the RMMM plan, particularly software bugs, incorrect quotation calculations, database errors, performance issues, and requirement misfit.
Defect Tracking & Feedback Loop	Identified issues will be recorded, assigned to the responsible member, corrected, and re-tested before approval.

Table 25: *Quality Assurance Plan*

6.5 Reviews and Audits

This section outlines how reviews and audits will be conducted to ensure that project deliverables and processes comply with agreed standards and requirements.

Key Area	Plan / Approach
Purpose	Ensure that all project activities, deliverables, and processes follow the required standards and meet the expectations of ExGen Battery Center & Car Wash.
Schedule	● Sprint Reviews: Conducted at the end of each sprint by the Scrum Master/Team Leader, Wane Summer Francisco, with participation from the QA Lead, Jewel Nerisha Tomale, and other team members. ● Mid-Project Audit: Conducted at the end of the requirements and design activities in October 2026 to review project progress and alignment with approved requirements. ● Pre-Deployment Audit: Conducted before the final deployment and user training to verify that the system, documentation, and testing outputs are ready for release. ● Post-Deployment Review: Conducted before the project closure on April 7, 2027 to assess system performance, user feedback, remaining issues, and completion of project deliverables.
Resources	● Scrum Master/Team Leader (Wane Summer Francisco): Oversees project reviews and ensures that necessary

	corrections are addressed. ● QA Lead (Jewel Nerisha Tomale): Manages quality reviews, testing records, and audit results. ● Technical Developer/System Designer (Junray Alfanta): Performs technical and interface checks and addresses coding or system issues. ● Client (Mr. Wendale Ajero): Provides feedback on system features during demonstrations and reviews. ● Project Adviser: Provides external feedback during major milestone reviews.
Review Methods	● Peer Reviews: Team members review source-code changes through GitHub and project documents through Google Drive. ● Walkthroughs: Conducted during team meetings to discuss system progress, clarify requirements, and review completed work. ● Document Reviews: The QA Lead reviews documents such as the SRS, SDD, test documents, and other required project outputs. ● Client Feedback Sessions: Client comments and recommendations are documented after system demonstrations and consultations.

Audit Methods	• Compliance Audits: The QA Lead checks whether system outputs align with the approved Software Requirements Specification (SRS). • Configuration Audits: The Technical Developer checks whether source-code versions and approved changes are properly tracked through GitHub. • Process Audits: The Process Manager verifies that the team is following the Agile Scrum process and approved project procedures.
Procedures	Define the scope of the review → conduct inspection of code, documents, system functions, and processes → record findings in Google Docs or Google Sheets → recommend improvements → apply corrections → verify the corrections during the succeeding sprint or review.
External Audits	When required, the client or project adviser may participate in external reviews to assess usability, functionality, documentation, and compliance with the business requirements of ExGen Battery Center & Car Wash.
Integration with QC	Reviews and audits will be integrated with the quality control activities managed by the QA Lead. Findings will be documented and tracked, and necessary corrections will be completed and verified before the team proceeds to the next major sprint or milestone.

Table 26: *Reviews and Audits Table*

6.6 Problem Resolution Plan

This section outlines the resources, methods, tools, techniques, and procedures to be used in reporting, analyzing, prioritizing, and processing software problem reports generated during the project development.

Key Area	Plan/Approach
Purpose	○ The Team Leader ensures that the team follows a clear step by step plan when a problem occurs. The team uses project documents to guide actions and prepare for any issue.
Meetings & Reporting	○ Team members may raise process related problems during weekly meetings facilitated by the Team Leader. ○ Scheduled meetings with the stakeholders and the project adviser also help to identify and solve the problems. These meetings allow discussions about system issues, miscommunications, member conflicts, and project misunderstandings which ensures that both technical and internal issues are handled properly.
Internal Issue Handling	○ Internal issues such as unclear responsibilities, misunderstandings of tasks, lack of contribution, or conflicts between team members are reported directly to the Team Leader or discussed during meetings. The Team Leader and Process Manager will handle reviewing the issue and decide the best solution to prevent delays and maintain smooth teamwork. For more information refer to Section 4.3.2 Schedule Control Plan.
External Issues Handling	○ External issues such as client concerns, unclear

	requirements, or third-party problems are reported to the Client Liaison. The Client Liaison coordinates with the client or external groups, while the Team Leader decides the best response.
Testing Issues	○ During the testing phase, the QA Tester and Team Leader performs initial testing to identify functional errors and UI inconsistencies before the client's user acceptance testing (UAT). Any issue found is documented, reviewed, and added to the list of problems to be resolved. This helps the team identify technical issues early and understand possible risks. Refer to Section 4.3.4 Quality Control Plan
Resolution Procedures	○ Once a problem is reported, the Team Leader assigns it to the appropriate member. The Technical Developer handles technical issues, while the Process Manager manages process-related concerns. The Team Leader monitors progress and ensures the issue is fully resolved before marking it complete.
User Feedback Handling	○ Feedback from the client and staff during UAT is documented in Google Docs and reviewed by the Process Manager and Team Leader. The Client Liaison communicates all client concerns to the team, and the feedback is used to guide necessary improvements.

Table 27: *Problem Resolution Plan*

6.7 Subcontractor Management Plan

The project will not be hiring or working with subcontractors. All project tasks, including planning, system design, development, testing, documentation, and deployment of the Web-Based Quotation and Billing System for ExGen Battery Center & Car Wash, will be handled solely by the project team members.

6.8 Process Improvement Plan

This section describes how the project team will review project processes, identify problems, and implement improvements during the development of the Web-Based Quotation and Billing System for ExGen Battery Center & Car Wash. The approach follows an iterative cycle to support continuous improvement throughout the project.

Step / Phase	Plan / Approach
1. Process Mapping (Plan)	Document and map the project workflow based on the Agile Scrum methodology. Identify each sprint, including its activities, inputs, outputs, and assigned responsibilities.
2. Problem Identification (Do)	Gather issues from testing, reviews, team discussions, and client feedback. Identify possible delays, communication problems, technical difficulties, or challenges in completing tasks.
3. Root Cause Analysis (Check)	Analyze identified issues through team discussions, brainstorming, the 5 Whys method, or cause-and-effect analysis to determine their underlying causes.

4. Process Redesign (Act)	Develop appropriate improvements such as reassigning tasks, adjusting workloads, providing additional training, improving communication, or using more suitable tools and methods.
5. Implementation	Apply the approved corrective actions within the Agile sprint cycle. Update project documentation, procedures, or workflows when necessary.
6. Monitoring & Evaluation	Monitor the results of implemented improvements using measures such as task completion time, defect or error rates, sprint completion, and client feedback.
7. Continuous Feedback	Maintain continuous improvement by reviewing changes, refining them when needed, and applying lessons to future sprints.

Table 28: *Process Improvement Plan*

7. Additional Plans

RMMM Traceability Matrix

The RMMM Traceability Matrix identifies and classifies the potential project, technical, and business risks associated with the ExGen Battery Center & Car Wash: Web-based Quotation & Billing System. Each risk is assigned a unique identification number, description, and priority level. The matrix is used to support risk mitigation, monitoring, and management throughout the project.

Probability Level (%)	Description	Priority Level
1-20%	Very Low	5
21-40%	Low	4
41-60%	Medium	3
61-80%	High	2
81-99%	Very High	1

Project Risks			
Risk ID	**Risk Name**	**Description**	**Priority**
PR-01	Schedule Delay	Project activities may not be completed according to the planned schedule.	2
PR-02	Budget Overrun	Project expenses may exceed the approved budget.	2
PR-03	Insufficient Team Members	There may be insufficient personnel to complete assigned project tasks.	2
PR-04	Poor Communication	Miscommunication among team members may cause errors or delays.	2
PR-05	Team Member Absenteeism	A team member may be unavailable during important project activities.	2
PR-06	Low Productivity	Assigned tasks may not be completed within the expected time.	2
PR-07	Lack of Training	Team members may lack sufficient knowledge or skills for assigned tasks.	2

PR-08	Member Turnover	A team member may leave or become unavailable during the project.	2
PR-09	Scope Creep	Additional requirements may be added beyond the agreed project scope.	1
PR-10	Resource Shortage	Required project resources may not be available when needed.	2
PR-11	Poor Time Management	Project time may not be properly allocated among activities.	2
PR-12	Team Conflict	Disagreements among team members may affect project progress.	2
PR-13	Unclear Requirements	Project requirements may not be clearly understood by the team.	1
PR-14	Client Delays	Delayed client responses or decisions may affect project activities.	2
PR-15	Data Loss	Important project files or records may be lost.	1
PR-16	Overlapping Tasks	Team members may perform the same or overlapping tasks.	3
PR-17	Wrong Estimates	Project time or resource	2

		requirements may be estimated incorrectly.	
PR-18	Incomplete Documentation	Required project documentation may be incomplete.	2
PR-19	Poor Task Assignment	Tasks may not be properly assigned according to team responsibilities.	2
PR-20	Client Indecision	Client decisions may be delayed and affect project progress.	2
PR-21	Delayed Requirement Approval	Project requirements may not be approved on time.	2
PR-22	Incomplete Meeting Records	Important decisions made during meetings may not be properly documented.	3
PR-23	Poor Task Tracking	Project task progress may not be properly monitored.	2
PR-24	Unrealistic Deadlines	Project activities may be given insufficient time for completion.	2
PR-25	Poor Workload Distribution	Workload may be distributed unevenly among team members.	2
PR-26	Lack of Backup Personnel	There may be no replacement available	2

		for an unavailable key team member.	
PR-27	Failure to Follow Project Process	Team members may fail to follow the agreed project procedures.	3
PR-28	Missed Project Milestones	Important project milestones may not be completed on time.	1
PR-29	Inconsistent Team Availability	Different schedules may affect team coordination.	2
PR-30	Delayed Documentation	Project documents may not be prepared or submitted on time.	2
PR-31	Incomplete Project Deliverables	Required project outputs may be incomplete.	1
PR-32	Frequent Schedule Changes	Frequent changes to the project schedule may disrupt planned activities.	2
PR-33	Poor Client Coordination	Insufficient coordination with the client may cause project issues.	2
PR-34	Lack of Adviser Consultation	Required guidance from the adviser may not be obtained.	3
PR-35	Delayed Adviser Feedback	Delayed adviser feedback may affect	2

		revisions and project progress.	
PR-36	Unapproved Requirement Changes	Requirements may be changed without proper approval.	1
PR-37	Duplicate Work	The same project task may be completed more than once.	3
PR-38	Unclear Project Priorities	The team may not clearly understand which tasks should be prioritized.	2
PR-39	Poor Meeting Attendance	Team members may miss important project information due to absence from meetings.	3
PR-40	Loss of Project Records	Important project records may become unavailable or misplaced.	1
PR-41	Incomplete Progress Reports	Progress reports may provide incomplete or inaccurate project status.	2
PR-42	Poor Risk Tracking	Identified risks may not be regularly reviewed or updated.	2
PR-43	Failure to Escalate Issues	Serious project problems may not be reported to the	2

		appropriate person on time.	
PR-44	Excessive Rework	Completed work may need to be repeated because of errors or changes.	2
PR-45	Poor Sprint Planning	Sprint activities may not be properly planned and assigned.	2
PR-46	Lack of Task Ownership	Responsibility for specific tasks may not be clearly assigned.	2
PR-47	Delayed Decision Making	Important project decisions may take too long to finalize.	2
PR-48	Insufficient Project Review	Project outputs may not be reviewed sufficiently before completion.	2
PR-49	Inconsistent Work Quality	Deliverables may have inconsistent levels of quality.	2
PR-50	Failure to Complete Required Documentation	Required documentation may be missing before project submission.	1

Table 29: *RMMM Traceability for Technical Risk*

Field	**Value**
Risk ID	PR-01
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Schedule Delay
Description	Project activities may not be completed according to the planned schedule.
Refinement/Context	Delays may happen when tasks take longer than expected, team members are unavailable, or previous activities are not completed on time.
Mitigation/Monitoring	Track task deadlines using the project schedule and review task progress during regular team meetings.
Management/ Contingency Plan/Trigger	If a task becomes delayed, the schedule will be reviewed, tasks may be reassigned, and delayed activities will be prioritized. Trigger: A task remains delayed or affects a project milestone.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 30: *RIS item No.1 Project Risks*

Risk ID	PR-02
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Budget Overrun
Description	Project expenses may exceed the approved budget.
Refinement/Context	Additional project expenses may reduce the resources available for completing the project.
Mitigation/Monitoring	Track project expenses regularly and review planned and actual expenses.
Management/Contingency Plan/Trigger	If expenses approach or exceed the available budget, unnecessary expenses will be reduced and resources will be reviewed. Trigger: Project expenses exceed the planned budget.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 31: *RIS item No.2 Project Risks*

Risk ID	PR-03
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Insufficient Team Members
Description	There may be insufficient personnel to complete assigned project tasks.
Refinement/Context	The project may be affected if team members become unavailable or if the workload becomes too large for the available members.
Mitigation/Monitoring	Monitor team availability and workload and review task assignments regularly.
Management/Contingency Plan/Trigger	If there are not enough available members, tasks will be redistributed among available team members. Trigger: Important tasks remain unassigned because of limited personnel.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 32: *RIS item No.3 Project Risks*

Risk ID	PR-04
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor Communication
Description	Miscommunication among team members may cause errors or delays.
Refinement/Context	Important instructions, decisions, or project updates may not be properly communicated to all members.
Mitigation/Monitoring	Use agreed communication channels and discuss important project updates during regular meetings.
Management/Contingency Plan/Trigger	If miscommunication occurs, the information will be clarified and important decisions will be documented. Trigger: Miscommunication causes an error or delay.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 33: *RIS item No.4 Project Risks*

Risk ID	PR-05
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Team Member Absenteeism
Description	A team member may be unavailable during important project activities.
Refinement/Context	Absence during meetings, development, testing, or consultations may affect project progress.
Mitigation/Monitoring	Monitor team availability and communicate important schedules and activities in advance.
Management/Contingency Plan/Trigger	If a member is absent, urgent tasks will be temporarily reassigned and the absent member will be updated. Trigger: Absence affects an important project activity.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 34: *RIS item No.5 Project Risks*

Risk ID	PR-06
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Low Productivity
Description	Assigned tasks may not be completed within the expected time.
Refinement/Context	Low productivity may occur because of workload, unclear tasks, technical difficulties, or poor time management.
Mitigation/Monitoring	Track task progress regularly and review unfinished tasks during team meetings.
Management/Contingency Plan/Trigger	If productivity becomes low, the cause will be identified and task assignments or deadlines may be adjusted. Trigger: Assigned tasks repeatedly remain unfinished past their deadlines.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 35: *RIS item No.6 Project Risks*

Risk ID	PR-07
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Lack of Training
Description	Team members may lack sufficient knowledge or skills for assigned tasks.
Refinement/Context	Some project activities may require technical or process knowledge that a team member does not yet have.
Mitigation/Monitoring	Provide guidance, share learning resources, and encourage team members to consult each other.
Management/ Contingency Plan/Trigger	If a member cannot complete a task because of a skill gap, a member with the needed knowledge will provide assistance. Trigger: A task cannot proceed because the assigned member lacks the required skills.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 36: *RIS item No.7 Project Risks*

Risk ID	PR-08
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Member Turnover
Description	A team member may leave or become unavailable during the project.
Refinement/Context	The loss of a member may affect tasks that depend on their knowledge or responsibilities.
Mitigation/Monitoring	Keep important project information documented and monitor team availability.
Management/Contingency Plan/Trigger	If a member becomes unavailable, their tasks will be reassigned and necessary project information will be transferred. Trigger: A team member leaves or becomes unavailable.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 37: *RIS item No.8 Project Risks*

Risk ID	PR-09
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Scope Creep
Description	Additional requirements may be added beyond the agreed project scope.
Refinement/Context	New features or changes requested during development may increase workload and affect the schedule.
Mitigation/Monitoring	Document and review requirements and discuss requested changes with the client before development.
Management/Contingency Plan/Trigger	If a new requirement is requested, its effect on time, resources, and scope will be reviewed before acceptance. Trigger: A requirement is requested outside the agreed scope.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 38: *RIS item No.9 Project Risks*

Risk ID	PR-10
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Resource Shortage
Description	Required project resources may not be available when needed.
Refinement/Context	The project may require hardware, software, internet access, hosting, or other resources.
Mitigation/Monitoring	Identify required resources early and check their availability throughout the project.
Management/Contingency Plan/Trigger	If a resource becomes unavailable, an available alternative will be identified or the task schedule will be adjusted. Trigger: A required project resource is unavailable.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 39: *RIS item No.10 Project Risks*

Risk ID	PR-11
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor Time Management
Description	Project time may not be properly allocated among activities.
Refinement/Context	Team members may spend too much time on one task and have insufficient time for other required activities.
Mitigation/Monitoring	Track task deadlines and review progress against the project schedule.
Management/Contingency Plan/Trigger	If time is not properly managed, tasks will be reprioritized and the schedule will be adjusted. Trigger: Tasks repeatedly exceed their planned time.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale — Scheduler / Time Manager

Table 40: *RIS item No.11 Project Risks*

Risk ID	PR-12
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Team Conflict
Description	Disagreements among team members may affect project progress.
Refinement/Context	Differences in opinions, responsibilities, or decisions may delay project activities.
Mitigation/Monitoring	Discuss concerns during meetings and clarify responsibilities and decisions.
Management/Contingency Plan/Trigger	If conflict affects project work, the Scrum Master / Team Leader will help the members reach an agreed solution. Trigger: Conflict causes a delay or prevents a task from progressing.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 41: *RIS item No.12 Project Risks*

Risk ID	PR-13
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Unclear Requirements
Description	Project requirements may not be clearly understood by the team.
Refinement/Context	Unclear requirements may result in incorrect system functions or unnecessary revisions.
Mitigation/Monitoring	Document, review, and clarify requirements with the client.
Management/Contingency Plan/Trigger	If a requirement is unclear, development of the affected function will be reviewed until the requirement is clarified. Trigger: A requirement cannot be clearly interpreted or implemented.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 42: *RIS item No.13 Project Risks*

Risk ID	PR-14
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Client Delays
Description	Delayed client responses or decisions may affect project activities.
Refinement/Context	The team may need client feedback or approval before continuing with certain requirements or prototype revisions.
Mitigation/Monitoring	Track client consultations and pending decisions.
Management/Contingency Plan/Trigger	If feedback is delayed, the team will follow up and continue other tasks that do not depend on the pending decision. Trigger: A client response delays a dependent activity.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 43: *RIS item No.14 Project Risks*

Risk ID	PR-15
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Data Loss
Description	Important project files or records may be lost.
Refinement/Context	Project files may be lost because of accidental deletion, device problems, or improper file management.
Mitigation/Monitoring	Back up important project files and store them in the agreed project storage location.
Management/Contingency Plan/Trigger	If files are lost, the latest available backup will be restored and the recovered files will be verified. Trigger: Important project files become unavailable or are accidentally deleted.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 44: *RIS item No.15 Project Risks*

Risk ID	PR-16
Date	21-Sep-26
Probability	41–60% (Medium)
Impact	Medium
Priority	3
Risk Name	Overlapping Tasks
Description	Team members may perform the same or overlapping tasks.
Refinement/Context	Unclear task ownership may cause duplicate work and wasted time.
Mitigation/Monitoring	Document task assignments and review responsibilities during project meetings.
Management/Contingency Plan/Trigger	If overlapping tasks are identified, responsibilities will be clarified and duplicate work will be stopped. Trigger: Two or more members are working on the same task.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 45: *RIS item No.16 Project Risks*

Risk ID	PR-17
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Wrong Estimates
Description	Project time or resource requirements may be estimated incorrectly.
Refinement/Context	Tasks may take longer or require more resources than originally expected.
Mitigation/Monitoring	Review task estimates and compare estimated time with actual project progress.
Management/Contingency Plan/Trigger	If estimates are incorrect, the schedule or resource allocation will be revised. Trigger: A task requires significantly more time or resources than estimated.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 46: *RIS item No.17 Project Risks*

Risk ID	PR-18
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Incomplete Documentation
Description	Required project documentation may be incomplete.
Refinement/Context	Missing documentation may affect project tracking, evaluation, or final submission.
Mitigation/Monitoring	Use a documentation checklist and review required documents regularly.
Management/Contingency Plan/Trigger	If documentation is incomplete, missing sections will be identified and completed before submission. Trigger: A required document or section is missing.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 47: *RIS item No.18 Project Risks*

Risk ID	PR-19
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor Task Assignment
Description	Tasks may not be properly assigned according to team responsibilities.
Refinement/Context	Incorrect task assignments may cause delays or result in work being assigned to someone without the required skills.
Mitigation/Monitoring	Assign tasks according to team roles and review assignments during team meetings.
Management/Contingency Plan/Trigger	If a task is incorrectly assigned, it will be reassigned to the appropriate team member. Trigger: A task is assigned to an inappropriate or unavailable member.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 48: *RIS item No.19 Project Risk*

Risk ID	PR-20
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Client Indecision
Description	Client decisions may be delayed and affect project progress.
Refinement/Context	The project may be delayed when the team is waiting for decisions regarding requirements, design, or system functions.
Mitigation/Monitoring	Record pending client decisions and monitor decisions that affect project activities.
Management/Contingency Plan/Trigger	If a decision is delayed, the team will follow up with the client and continue unaffected project activities. Trigger: A pending decision prevents a project activity from continuing.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 49: *RIS item No.20 Project Risk*

Risk ID	PR-21
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Delayed Requirement Approval
Description	Project requirements may not be approved on time.
Refinement/Context	Delayed approval may prevent the team from proceeding with development or revisions.
Mitigation/Monitoring	Follow up on pending approvals and maintain a list of requirements awaiting confirmation.
Management/Contingency Plan/Trigger	If approval is delayed, adjust the affected tasks and prioritize activities that can proceed without approval.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 50: *RIS item No.21 Project Risk*

Risk ID	PR-22
Date	21-Sep-26
Probability	41–60% (Medium)
Impact	Medium
Priority	3
Risk Name	Incomplete Meeting Records
Description	Important decisions made during meetings may not be properly documented.
Refinement/Context	Missing meeting records may cause confusion about decisions, assignments, and requirements.
Mitigation/Monitoring	Record meeting discussions, decisions, assigned tasks, and important updates after every meeting.
Management/Contingency Plan/Trigger	If meeting information is missing, confirm the decisions with team members and update the meeting records.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 51: *RIS item No.22 Project Risk*

Risk ID	PR-23
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor Task Tracking
Description	Project task progress may not be properly monitored.
Refinement/Context	Tasks may be delayed or forgotten when their progress is not regularly tracked.
Mitigation/Monitoring	Update the task tracker regularly and review task progress during team meetings.
Management/Contingency Plan/Trigger	If tasks are found to be delayed, identify the cause and reassign or adjust the schedule when necessary.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 52: *RIS item No.23 Project Risk*

Risk ID	PR-24
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Unrealistic Deadlines
Description	Project activities may be given insufficient time for completion.
Refinement/Context	Short deadlines may cause rushed work, missed requirements, or reduced quality.
Mitigation/Monitoring	Review task estimates and compare deadlines with the team's available time and workload.
Management/Contingency Plan/Trigger	If a deadline cannot be met, adjust the schedule and prioritize critical activities.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 53: *RIS item No.24 Project Risk*

Risk ID	PR-25
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor Workload Distribution
Description	Workload may be distributed unevenly among team members.
Refinement/Context	Uneven workloads may cause delays and reduce the team's ability to complete assigned tasks.
Mitigation/Monitoring	Review task assignments and workload regularly and redistribute tasks when necessary.
Management/Contingency Plan/Trigger	If a member becomes overloaded, transfer suitable tasks to available team members.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 54: *RIS item No.25 Project Risk*

Risk ID	PR-26
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Lack of Backup Personnel
Description	There may be no replacement available for an unavailable key team member.
Refinement/Context	A key member's absence may interrupt activities that depend on their knowledge or responsibilities.
Mitigation/Monitoring	Share important project information and document tasks so other members can understand the work.
Management/Contingency Plan/Trigger	If a key member becomes unavailable, reassign their tasks to another available member.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco – Scrum Master / Team Leader

Table 55: *RIS item No.26 Project Risk*

Risk ID	PR-27
Date	21-Sep-26
Probability	41–60% (Medium)
Impact	Medium
Priority	3
Risk Name	Failure to Follow Project Process
Description	Team members may fail to follow the agreed project procedures.
Refinement/Context	Failure to follow agreed procedures may cause inconsistent work and project delays.
Mitigation/Monitoring	Review the agreed workflow, responsibilities, and procedures with team members.
Management/Contingency Plan/Trigger	If the process is not followed, identify the cause and remind or guide the responsible member on the required procedure.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta – Process Manager

Table 56: *RIS item No.27 Project Risk*

Risk ID	PR-28
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Missed Project Milestones
Description	Important project milestones may not be completed on time.
Refinement/Context	Missed milestones may affect succeeding activities and the overall project schedule.
Mitigation/Monitoring	Track milestone dates and review progress regularly.
Management/Contingency Plan/Trigger	If a milestone is missed, identify delayed activities and revise the schedule to recover lost time.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 57: *RIS item No.28 Project Risk*

Risk ID	PR-29
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Inconsistent Team Availability
Description	Different schedules may affect team coordination.
Refinement/Context	Different availability may make meetings, collaboration, and task completion difficult.
Mitigation/Monitoring	Maintain an updated team schedule and coordinate meeting times in advance.
Management/Contingency Plan/Trigger	If a member is unavailable, adjust meeting times or reassign urgent tasks when needed.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 58: *RIS item No.29 Project Risk*

Risk ID	PR-30
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Delayed Documentation
Description	Project documents may not be prepared or submitted on time.
Refinement/Context	Delayed documentation may affect project submissions, reviews, and record keeping.
Mitigation/Monitoring	Set documentation deadlines and regularly check the status of required documents.
Management/Contingency Plan/Trigger	If documentation is delayed, prioritize the required document and assign additional support when necessary.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 59: *RIS item No.30 Project Risk*

Risk ID	PR-31
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Incomplete Project Deliverables
Description	Required project outputs may be incomplete.
Refinement/Context	Incomplete deliverables may prevent the project from meeting its required objectives or submission requirements.
Mitigation/Monitoring	Use a deliverable checklist and review completed outputs against the project requirements.
Management/Contingency Plan/Trigger	If a deliverable is incomplete, identify the missing parts and prioritize their completion before submission.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco – Scrum Master / Team Leader

Table 60: *RIS item No.31 Project Risk*

Risk ID	PR-32
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Frequent Schedule Changes
Description	Frequent changes to the project schedule may disrupt planned activities.
Refinement/Context	Repeated schedule changes may cause conflicts and delays in planned tasks.
Mitigation/Monitoring	Keep the project schedule updated and review proposed changes before applying them.
Management/Contingency Plan/Trigger	If schedule changes become necessary, inform the team and adjust affected tasks and deadlines.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 61: *RIS item No.32 Project Risk*

Risk ID	PR-33
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor Client Coordination
Description	Insufficient coordination with the client may cause project issues.
Refinement/Context	Limited communication with the client may result in unclear requirements, delayed feedback, or incorrect assumptions.
Mitigation/Monitoring	Maintain regular communication with the client and document important discussions and decisions.
Management/Contingency Plan/Trigger	If coordination problems occur, schedule a discussion with the client to clarify requirements and decisions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 62: *RIS item No.33 Project Risk*

Risk ID	PR-34
Date	21-Sep-26
Probability	41–60% (Medium)
Impact	Medium
Priority	3
Risk Name	Lack of Adviser Consultation
Description	Required guidance from the adviser may not be obtained.
Refinement/Context	Lack of consultation may cause the team to continue with unclear or incorrect project decisions.
Mitigation/Monitoring	Schedule adviser consultations and prepare questions or concerns before meetings.
Management/Contingency Plan/Trigger	If guidance is not obtained, identify affected decisions and request consultation before proceeding with critical work.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 63: *RIS item No.34 Project Risk*

Risk ID	PR-35
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Delayed Adviser Feedback
Description	Delayed adviser feedback may affect revisions and project progress.
Refinement/Context	Delayed feedback may prevent the team from finalizing documents, designs, or system outputs.
Mitigation/Monitoring	Submit materials for review early and maintain a record of pending feedback.
Management/Contingency Plan/Trigger	If feedback is delayed, continue with unaffected tasks and adjust the revision schedule when feedback is received.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 64: *RIS item No.35 Project Risk*

Risk ID	PR-36
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Unapproved Requirement Changes
Description	Requirements may be changed without proper approval.
Refinement/Context	Unapproved changes may cause scope issues, rework, and inconsistencies between requirements and development.
Mitigation/Monitoring	Document requirement changes and require confirmation before implementing them.
Management/Contingency Plan/Trigger	If an unapproved change is identified, stop the affected work and confirm the requirement with the responsible person.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 65: *RIS item No.36 Project Risk*

Risk ID	PR-37
Date	21-Sep-26
Probability	41–60% (Medium)
Impact	Medium
Priority	3
Risk Name	Duplicate Work
Description	The same project task may be completed more than once.
Refinement/Context	Duplicate work wastes project time and may create inconsistent outputs.
Mitigation/Monitoring	Keep task assignments updated and communicate task ownership among team members.
Management/Contingency Plan/Trigger	If duplicate work is discovered, compare the outputs and retain the appropriate version.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 66: *RIS item No.37 Project Risk*

Risk ID	PR-38
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Unclear Project Priorities
Description	The team may not clearly understand which tasks should be prioritized.
Refinement/Context	Unclear priorities may cause important tasks to be delayed while less important tasks are completed first.
Mitigation/Monitoring	Review task priorities during planning and team meetings.
Management/Contingency Plan/Trigger	If priorities become unclear, the team leader will clarify the order of tasks and update assignments.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 67: *RIS item No.38 Project Risk*

Risk ID	PR-39
Date	21-Sep-26
Probability	41–60% (Medium)
Impact	Medium
Priority	3
Risk Name	Poor Meeting Attendance
Description	Team members may miss important project information due to absence from meetings.
Refinement/Context	Absence from meetings may cause members to miss decisions, task assignments, or project updates.
Mitigation/Monitoring	Inform members about meetings in advance and record important meeting information.
Management/Contingency Plan/Trigger	If a member misses a meeting, provide the meeting records and communicate their assigned tasks or decisions.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 68: *RIS item No.39 Project Risk*

Risk ID	PR-40
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Loss of Project Records
Description	Important project records may become unavailable or misplaced.
Refinement/Context	Lost records may affect project tracking, documentation, requirements, and submission preparation.
Mitigation/Monitoring	Store project records in an organized shared location and maintain backup copies.
Management/Contingency Plan/Trigger	If records are lost, recover them from available backups or previous versions.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 69: *RIS item No.40 Project Risk*

Risk ID	PR-41
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Incomplete Progress Reports
Description	Progress reports may provide incomplete or inaccurate project status.
Refinement/Context	Incomplete reports may make it difficult to determine actual project progress and remaining work.
Mitigation/Monitoring	Collect updates from team members and review progress reports before submission.
Management/Contingency Plan/Trigger	If a report is incomplete, request the missing information and update the report before submission.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 70: *RIS item No.41 Project Risk*

Risk ID	PR-42
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor Risk Tracking
Description	Identified risks may not be regularly reviewed or updated.
Refinement/Context	Unmonitored risks may become serious before the team recognizes changes in their status.
Mitigation/Monitoring	Review the risk register regularly and update risk status and actions.
Management/Contingency Plan/Trigger	If a risk increases in severity, update its priority and apply the appropriate contingency action.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 71: *RIS item No.42 Project Risk*

Risk ID	PR-43
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Failure to Escalate Issues
Description	Serious project problems may not be reported to the appropriate person on time.
Refinement/Context	Unreported issues may continue and cause greater delays or project problems.
Mitigation/Monitoring	Encourage team members to report serious issues immediately and define who should receive escalated concerns.
Management/Contingency Plan/Trigger	If a serious issue is not resolved by the assigned member, escalate it to the team leader or appropriate adviser.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 72: *RIS item No.43 Project Risk*

Risk ID	PR-44
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Excessive Rework
Description	Completed work may need to be repeated because of errors or changes.
Refinement/Context	Repeated revisions may consume project time and delay other activities.
Mitigation/Monitoring	Review requirements and completed work before finalizing outputs to reduce avoidable errors.
Management/Contingency Plan/Trigger	If excessive rework occurs, identify the cause and prioritize the affected work before continuing with lower-priority tasks.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 73: *RIS item No.44 Project Risk*

Risk ID		PR-45
Date		21-Sep-26
Probability		61–80% (High)
Impact		Medium
Priority		2
Risk Name		Poor Sprint Planning
Description		Sprint activities may not be properly planned and assigned.
Refinement/Context		Poor sprint planning may result in unclear tasks, unrealistic workloads, and missed sprint objectives.
Mitigation/Monitoring		Review sprint objectives, tasks, responsibilities, and available time before starting each sprint.
Management/Contingency Plan/Trigger		If sprint activities are not achievable, reprioritize tasks and adjust assignments.
Current Status		Monitoring
Originator		Project Team
Assigned		Wane Summer Francisco

Table 74: *RIS item No.45 Project Risk*

Risk ID	PR-46
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Lack of Task Ownership
Description	Responsibility for specific tasks may not be clearly assigned.
Refinement/Context	Unclear ownership may result in tasks being delayed, duplicated, or left unfinished.
Mitigation/Monitoring	Assign a responsible team member to each task and maintain an updated task list.
Management/Contingency Plan/Trigger	If a task has no clear owner, assign responsibility immediately and update the task tracker.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 75: *RIS item No.46 Project Risk*

Risk ID	PR-47
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Delayed Decision Making
Description	Important project decisions may take too long to finalize.
Refinement/Context	Delayed decisions may prevent the team from completing dependent activities.
Mitigation/Monitoring	Identify decisions that need approval and follow up on pending decisions.
Management/Contingency Plan/Trigger	If a decision remains unresolved, escalate it to the appropriate person and adjust affected tasks.
Current Status	Monitoring
Originator	Project Team
Assigned	Wane Summer Francisco

Table 76: *RIS item No.47 Project Risk*

Risk ID	PR-48
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Insufficient Project Review
Description	Project outputs may not be reviewed sufficiently before completion.
Refinement/Context	Insufficient review may allow errors or missing requirements to remain in the final deliverables.
Mitigation/Monitoring	Conduct regular reviews and use checklists to verify project requirements and outputs.
Management/Contingency Plan/Trigger	If errors are found during final review, prioritize corrections before project submission.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale – QA Lead

Table 77: *RIS item No.48 Project Risk*

Risk ID	PR-49
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Inconsistent Work Quality
Description	Deliverables may have inconsistent levels of quality.
Refinement/Context	Different quality levels among project outputs may affect the consistency of the final project.
Mitigation/Monitoring	Use agreed standards and review deliverables before considering them complete.
Management/Contingency Plan/Trigger	If quality problems are identified, return the affected output for correction and review it again.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 78: *RIS item No.49 Project Risk*

Risk ID	PR-50
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Failure to Complete Required Documentation
Description	Required documentation may be missing before project submission.
Refinement/Context	Missing documentation may prevent the project from satisfying submission and project requirements.
Mitigation/Monitoring	Use a documentation checklist and regularly verify that all required documents are completed.
Management/Contingency Plan/Trigger	If required documentation is missing, prioritize its completion and review it before submission.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 79: *RIS item No.50 Project Risk*

Technical Risks			
Risk ID	**Risk Name**	**Description**	**Priority**
TR-01	Software Bugs	Errors in the source code may cause incorrect system behavior.	1
TR-02	Incorrect Quotation Calculation	Quotation amounts may be calculated incorrectly by the system.	1
TR-03	Database Errors	Customer, product, service, or transaction records may be stored incorrectly or become missing.	1
TR-04	System Crash	The system may stop responding or become unavailable during use.	1
TR-05	Browser Compatibility	The system may not function correctly in some web browsers.	2
TR-06	Poor System Performance	The system may respond slowly during use.	2

TR-07	Security Vulnerability	The system may contain weaknesses that could allow unauthorized access or attacks.	1
TR-08	Backup Failure	System or database backups may fail to complete properly.	1
TR-09	Testing Errors	Software defects may not be identified during testing.	2
TR-10	Insufficient Technical Knowledge	Team members may lack the technical skills needed to develop or maintain the system.	2
TR-11	Code Management Problems	Source code may not be properly organized or maintained.	2
TR-12	Version Control Error	An incorrect or outdated version of the source code may be used.	2
TR-13	Data Integrity Failure	Database records may become incomplete, duplicated, or inconsistent.	1
TR-14	Requirement Misfit	The implemented system functions may not match the approved requirements.	1

TR-15	Limited Testing Time	There may be insufficient time to conduct complete system testing.	2
TR-16	Technology Obsolescence	Used technologies may become outdated during the project.	3
TR-17	Server Downtime	The hosting server may become temporarily unavailable.	2
TR-18	UI/UX Inconsistency	User interface elements may not have consistent layouts or behavior.	2
TR-19	Scalability Problem	The system may have difficulty handling increased users or records.	2
TR-20	Technical Documentation Gap	Technical documentation may be incomplete or outdated.	2
TR-21	Server Configuration Error	Incorrect server settings may cause system failures.	2
TR-22	PHP Configuration Error	Incorrect PHP settings may prevent system functions from working properly.	2
TR-23	MySQL Connection Failure	The application may fail to connect to the MySQL database.	1

TR-24	Incorrect Database Permissions	Database permissions may prevent required system operations.	1
TR-25	SQL Query Errors	Incorrect SQL queries may produce wrong or incomplete results.	1
TR-26	Invalid User Input	Invalid user input may not be processed correctly by the system.	2
TR-27	Form Validation Failure	The system may accept incomplete or invalid information.	1
TR-28	Session Management Error	User sessions may not be properly created, maintained, or terminated.	2
TR-29	Authentication Failure	User login verification may fail or behave incorrectly.	1
TR-30	Authorization Failure	Users may gain access to functions they are not authorized to use.	1
TR-31	Broken Navigation	Links or navigation controls may not work correctly.	2
TR-32	Missing System Links	Required pages or system functions may not be properly connected.	2

TR-33	Incorrect Booking Data	Customer booking information may be stored or displayed incorrectly.	1
TR-34	Incorrect Customer Data	Customer information may be stored or displayed incorrectly.	1
TR-35	Incorrect Product Data	Product information may be incorrect or improperly displayed.	2
TR-36	Incorrect Service Data	Service information may be incorrect or improperly displayed.	2
TR-37	Incorrect Billing Record	Billing information may be recorded incorrectly.	1
TR-38	Duplicate Transaction Records	A transaction may be recorded more than once.	1
TR-39	Missing Transaction Records	Completed transactions may not be properly recorded in the database.	1
TR-40	Incorrect Date and Time Handling	Dates or times may be stored or displayed incorrectly.	2
TR-41	File Upload Failure	Required files may fail to upload or be stored properly.	3

TR-42	Database Backup Corruption	A database backup may become corrupted and unusable.	1
TR-43	Slow Database Queries	Inefficient database queries may slow down system operations.	2
TR-44	Hosting Configuration Failure	Incorrect hosting configuration may prevent the system from operating correctly.	2
TR-45	Domain Configuration Problem	Domain configuration issues may prevent users from accessing the system.	3
TR-46	HTTPS/SSL Configuration Problem	Incorrect SSL configuration may cause security warnings or connection problems.	2
TR-47	Cross-Browser Display Error	System pages may display incorrectly in different browsers.	2
TR-48	Responsive Design Failure	System pages may not display properly on different screen sizes.	2
TR-49	Deployment Failure	The system may fail during deployment to the hosting environment.	1

TR-50	System Integration Failure	Different system components may fail to work together correctly.	1

Table 80: *RMMM Traceability for Technical Risk*

Risk ID	TR-01
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Software Bugs
Description	Errors in the source code may cause incorrect system behavior.
Refinement/Context	Code errors may cause system functions to produce incorrect results or fail during use.
Mitigation/Monitoring	Conduct regular code reviews and testing during development to identify errors early.
Management/Contingency Plan/Trigger	If a critical bug is found, identify the affected function, correct the code, and perform retesting.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 81: *RIS item No.1 Technical Risk*

Risk ID	TR-02
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Incorrect Quotation Calculation
Description	Quotation amounts may be calculated incorrectly by the system.
Refinement/Context	Incorrect calculations may result in inaccurate quotations being provided to customers.
Mitigation/Monitoring	Test quotation calculations using different products, services, quantities, and prices.
Management/Contingency Plan/Trigger	If an incorrect calculation is found, correct the calculation logic and retest affected quotation functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 82: *RIS item No.2 Technical Risk*

Risk ID	TR-03
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Database Errors
Description	Customer, product, service, or transaction records may be stored incorrectly or become missing.
Refinement/Context	Database errors may affect the accuracy and availability of important system records.
Mitigation/Monitoring	Validate database operations and regularly review stored records for errors or missing information.
Management/Contingency Plan/Trigger	If database errors occur, identify the affected records and restore or correct them using available backups.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta – Technical Developer

Table 83: *RIS item No.3 Technical Risk*

Risk ID	TR-04
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	System Crash
Description	The system may stop responding or become unavailable during use.
Refinement/Context	A system crash may interrupt customer transactions and staff activities.
Mitigation/Monitoring	Test system stability and monitor errors during development and deployment.
Management/Contingency Plan/Trigger	If the system crashes, identify the cause, restore the system, and test the affected functions before returning to normal operation.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 84: *RIS item No.4 Technical Risk*

Risk ID	TR-05
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Browser Compatibility
Description	The system may not function correctly in some web browsers.
Refinement/Context	Different browsers may interpret or display system functions differently.
Mitigation/Monitoring	Test the system using commonly used web browsers during development.
Management/Contingency Plan/Trigger	If compatibility problems are found, identify the affected browser and adjust the system code or interface.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta – Technical Developer

Table 85: *RIS item No.5 Technical Risk*

Risk ID	TR-06
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Poor System Performance
Description	The system may respond slowly during use.
Refinement/Context	Slow response may affect the user's ability to complete system activities efficiently.
Mitigation/Monitoring	Test system response times and review inefficient code or database operations.
Management/Contingency Plan/Trigger	If performance problems occur, optimize the affected functions, queries, or resources.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 86: *RIS item No.6 Technical Risk*

Risk ID	TR-07
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Security Vulnerability
Description	The system may contain weaknesses that could allow unauthorized access or attacks.
Refinement/Context	Security weaknesses may expose customer, business, or transaction information.
Mitigation/Monitoring	Apply secure coding practices, validate user input, and test authentication and authorization controls.
Management/Contingency Plan/Trigger	If a security vulnerability is identified, restrict the affected function, correct the vulnerability, and retest the system.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 87: *RIS item No.7 Technical Risk*

Risk ID	TR-08
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Backup Failure
Description	System or database backups may fail to complete properly.
Refinement/Context	Failed backups may prevent recovery of important system and database information.
Mitigation/Monitoring	Perform scheduled backups and verify that backup files can be accessed and restored.
Management/Contingency Plan/Trigger	If a backup fails, identify the cause and create a new verified backup as soon as possible.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 88: *RIS item No.8 Technical Risk*

Risk ID	TR-09
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Testing Errors
Description	Software defects may not be identified during testing.
Refinement/Context	Incomplete or incorrect testing may allow defects to remain in the system.
Mitigation/Monitoring	Use test cases and checklists and conduct repeated testing of important system functions.
Management/Contingency Plan/Trigger	If a defect is discovered after testing, document the issue, correct it, and perform regression testing.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 89: *RIS item No.9 Technical Risk*

Risk ID	TR-10
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Insufficient Technical Knowledge
Description	Team members may lack the technical skills needed to develop or maintain the system.
Refinement/Context	Limited technical knowledge may cause development errors or delays.
Mitigation/Monitoring	Identify technical knowledge gaps and provide documentation, practice, or guidance for needed technologies.
Management/Contingency Plan/Trigger	If a technical issue cannot be resolved, assign the task to a member with the required knowledge and research the needed solution.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 90: *RIS item No.10 Technical Risk*

Risk ID	TR-11
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Code Management Problems
Description	Source code may not be properly organized or maintained.
Refinement/Context	Poor code organization may make development, debugging, and maintenance more difficult.
Mitigation/Monitoring	Follow an agreed code structure, naming conventions, and repository organization.
Management/Contingency Plan/Trigger	If code management problems occur, reorganize affected files and establish clearer coding and repository practices.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 91: *RIS item No.11 Technical Risk*

Risk ID	TR-12
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Version Control Error
Description	An incorrect or outdated version of the source code may be used.
Refinement/Context	Using the wrong version may cause previous work to be overwritten or incorrect code to be deployed.
Mitigation/Monitoring	Use Git consistently and review commits and branches before merging or deploying changes.
Management/Contingency Plan/Trigger	If an incorrect version is used, restore the appropriate version from the repository and verify the affected changes.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 92: *RIS item No.12 Technical Risk*

Risk ID	TR-13
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Data Integrity Failure
Description	Database records may become incomplete, duplicated, or inconsistent.
Refinement/Context	Data integrity problems may cause inaccurate customer, product, service, quotation, or billing information.
Mitigation/Monitoring	Apply database validation rules and regularly check records for duplicates, missing values, and inconsistencies.
Management/Contingency Plan/Trigger	If data integrity problems occur, identify affected records and correct or restore them from verified data.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 93: *RIS item No.13 Technical Risk*

Risk ID	TR-14
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Requirement Misfit
Description	The implemented system functions may not match the approved requirements.
Refinement/Context	A mismatch between requirements and implementation may result in incorrect or incomplete system functions.
Mitigation/Monitoring	Review requirements during development and test system functions against approved requirements.
Management/Contingency Plan/Trigger	If a mismatch is found, identify the affected function and revise the implementation according to the approved requirement.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 94: *RIS item No.14 Technical Risk*

Risk ID	TR-15
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Limited Testing Time
Description	There may be insufficient time to conduct complete system testing.
Refinement/Context	Limited testing time may result in unresolved defects before project submission.
Mitigation/Monitoring	Plan testing activities early and prioritize critical system functions.
Management/Contingency Plan/Trigger	If testing time becomes limited, focus on high-priority functions and document remaining issues for correction.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 95: *RIS item No.15 Technical Risk*

Risk ID	TR-16
Date	21-Sep-26
Probability	41–60% (Medium)
Impact	Medium
Priority	3
Risk Name	Technology Obsolescence
Description	Used technologies may become outdated during the project.
Refinement/Context	Outdated technologies may cause compatibility, maintenance, or support problems.
Mitigation/Monitoring	Use currently supported technologies and monitor changes that may affect the project technology stack.
Management/Contingency Plan/Trigger	If a technology becomes unsuitable, identify a supported alternative and evaluate the changes needed.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 96: *RIS item No.16 Technical Risk*

Risk ID	TR-17
Date	21-Sep-26
Probability	61–80% (High)
Impact	High
Priority	2
Risk Name	Server Downtime
Description	The hosting server may become temporarily unavailable.
Refinement/Context	Server downtime may prevent users from accessing the web-based system.
Mitigation/Monitoring	Monitor hosting availability and maintain backup copies of important system and database files.
Management/Contingency Plan/Trigger	If the server becomes unavailable, check the hosting service and restore system availability when possible.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 97: *RIS item No.17 Technical Risk*

Risk ID	TR-18
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	UI/UX Inconsistency
Description	User interface elements may not have consistent layouts or behavior.
Refinement/Context	Inconsistent interfaces may confuse users or make system navigation more difficult.
Mitigation/Monitoring	Follow the approved interface design and review pages for consistent layouts, labels, and controls.
Management/Contingency Plan/Trigger	If inconsistencies are identified, update the affected interface elements and perform another review.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 98: *RIS item No.18 Technical Risk*

Risk ID	TR-19
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Scalability Problem
Description	The system may have difficulty handling increased users or records.
Refinement/Context	Increased data or users may cause slower performance or system limitations.
Mitigation/Monitoring	Use an organized database structure and test system performance with increased data where possible.
Management/Contingency Plan/Trigger	If scalability problems occur, identify the affected component and optimize the database or system functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 99: *RIS item No.19 Technical Risk*

Risk ID	TR-20
Date	21-Sep-26
Probability	61–80% (High)

Impact	Medium
Priority	2
Risk Name	Technical Documentation Gap
Description	Technical documentation may be incomplete or outdated.
Refinement/Context	Missing technical documentation may make system maintenance, troubleshooting, and future updates more difficult.
Mitigation/Monitoring	Update technical documentation as development changes are made.
Management/Contingency Plan/Trigger	If documentation is found to be incomplete, identify missing information and update it before project completion.
Current Status	Monitoring
Originator	Project Team
Assigned	Jewel Nerisha Tomale

Table 100: *RIS item No.20 Technical Risk*

Risk ID	TR-21
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Server Configuration Error
Description	Incorrect server settings may cause system failures.
Refinement/Context	Incorrect server settings may prevent the application from operating properly.
Mitigation/Monitoring	Review server configuration settings and test the system after configuration changes.
Management/Contingency Plan/Trigger	If a configuration error occurs, identify the incorrect setting, correct it, and retest the system.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 101: *RIS item No.21 Technical Risk*

Risk ID	TR-22
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	PHP Configuration Error
Description	Incorrect PHP settings may prevent system functions from working properly.
Refinement/Context	Incorrect PHP configuration may cause application errors or prevent required functions from operating.
Mitigation/Monitoring	Review PHP configuration settings and test required application functions.
Management/Contingency Plan/Trigger	If a PHP configuration problem occurs, identify the incorrect setting, correct it, and retest the affected functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 102: *RIS item No.22 Technical Risk*

Risk ID	TR-23
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	MySQL Connection Failure
Description	The application may fail to connect to the MySQL database.
Refinement/Context	A database connection failure may prevent the system from retrieving or saving information.
Mitigation/Monitoring	Test database connections regularly and verify database credentials and connection settings.
Management/Contingency Plan/Trigger	If the connection fails, check the database server, credentials, and connection configuration before restoring the affected functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 103: *RIS item No.23 Technical Risk*

Risk ID	TR-24
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Incorrect Database Permissions
Description	Database permissions may prevent required system operations.
Refinement/Context	Incorrect permissions may prevent the application from reading, inserting, updating, or managing required records.
Mitigation/Monitoring	Review database user permissions and test required database operations.
Management/Contingency Plan/Trigger	If required operations are blocked, correct the database permissions and retest the affected functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 104: *RIS item No.24 Technical Risk*

Risk ID	TR-25
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	SQL Query Errors
Description	Incorrect SQL queries may produce wrong or incomplete results.
Refinement/Context	Incorrect queries may affect customer records, quotations, billing information, and other system operations.
Mitigation/Monitoring	Test SQL queries using expected data and verify the returned results.
Management/Contingency Plan/Trigger	If a query error is found, correct the SQL statement and retest the affected database operation.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 105: *RIS item No.25 Technical Risk*

Risk ID	TR-26
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Invalid User Input
Description	Invalid user input may not be processed correctly by the system.
Refinement/Context	Invalid information entered by users may cause errors or incorrect system processing.
Mitigation/Monitoring	Apply input validation and test forms using valid and invalid input values.
Management/Contingency Plan/Trigger	If invalid input causes a problem, correct the validation or processing logic and retest the form.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 106: *RIS item No.26 Technical Risk*

Risk ID	TR-27
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Form Validation Failure
Description	The system may accept incomplete or invalid information.
Refinement/Context	Failure to validate forms may result in incomplete or incorrect records being stored.
Mitigation/Monitoring	Test required fields, input formats, and validation rules for all important forms.
Management/Contingency Plan/Trigger	If invalid information is accepted, correct the validation rules and retest the affected form.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 107: *RIS item No.27 Technical Risk*

Risk ID	TR-28
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium

Priority	2
Risk Name	Session Management Error
Description	User sessions may not be properly created, maintained, or terminated.
Refinement/Context	Session problems may cause users to lose access or remain logged in incorrectly.
Mitigation/Monitoring	Test login sessions, logout functions, session expiration, and access restrictions.
Management/Contingency Plan/Trigger	If session problems occur, correct the session handling logic and retest authentication and logout functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 108: *RIS item No.28 Technical Risk*

Risk ID	TR-29
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Authentication Failure
Description	User login verification may fail or behave incorrectly.
Refinement/Context	Authentication problems may prevent authorized users from accessing the system or allow incorrect login behavior.
Mitigation/Monitoring	Test valid and invalid login credentials and verify authentication controls.
Management/Contingency Plan/Trigger	If authentication fails, investigate the login process, correct the issue, and retest the authentication function.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 109: *RIS item No.29 Technical Risk*

Risk ID	TR-30
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1

Risk Name	Authorization Failure
Description	Users may gain access to functions they are not authorized to use.
Refinement/Context	Incorrect authorization may expose restricted system functions or information.
Mitigation/Monitoring	Test user roles and access permissions for each restricted system function.
Management/Contingency Plan/Trigger	If unauthorized access is identified, correct the access controls and immediately retest affected functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 110: *RIS item No.30 Technical Risk*

Risk ID	TR-31
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Broken Navigation
Description	Links or navigation controls may not work correctly.
Refinement/Context	Broken navigation may prevent users from reaching required pages or completing system activities.
Mitigation/Monitoring	Test all navigation links, buttons, and page transitions during system testing.
Management/Contingency Plan/Trigger	If navigation problems are found, correct the affected links or controls and retest the navigation flow.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 111: *RIS item No.30 Technical Risk*

Risk ID	TR-32
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Missing System Links
Description	Required pages or system functions may not be properly connected.
Refinement/Context	Missing connections may prevent users from completing related system processes.
Mitigation/Monitoring	Review system workflows and verify that required pages and functions are properly connected.
Management/Contingency Plan/Trigger	If a missing link is identified, connect the affected functions and test the complete workflow.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 112: *RIS item No.31 Technical Risk*

Risk ID	TR-33
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Incorrect Booking Data
Description	Customer booking information may be stored or displayed incorrectly.
Refinement/Context	Incorrect booking data may cause scheduling problems and incorrect customer service information.
Mitigation/Monitoring	Test booking forms and verify that booking information is correctly stored and displayed.
Management/Contingency Plan/Trigger	If incorrect booking data is found, correct the affected records or system logic and retest the booking process.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 113: *RIS item No.33 Technical Risk*

Risk ID	TR-34
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Incorrect Customer Data
Description	Customer information may be stored or displayed incorrectly.
Refinement/Context	Incorrect customer information may affect quotations, bookings, billing, and customer records.
Mitigation/Monitoring	Validate customer input and verify stored customer records during testing.
Management/Contingency Plan/Trigger	If incorrect customer information is identified, correct the record and determine whether other affected records need review.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 114: *RIS item No.34 Technical Risk*

Risk ID	TR-35
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Incorrect Product Data
Description	Product information may be incorrect or improperly displayed.
Refinement/Context	Incorrect product information may result in inaccurate product details or quotations.
Mitigation/Monitoring	Review product records and test product information displayed in the system.
Management/Contingency Plan/Trigger	If incorrect product information is found, correct the database record and verify affected quotation functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 115: *RIS item No.35 Technical Risk*

Risk ID	TR-36
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Incorrect Service Data
Description	Service information may be incorrect or improperly displayed.
Refinement/Context	Incorrect service information may affect customer selection, booking, and quotation details.
Mitigation/Monitoring	Review service records and test service information displayed throughout the system.
Management/Contingency Plan/Trigger	If incorrect service data is identified, correct the record and retest affected service and quotation functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 116: *RIS item No.36 Technical Risk*

Risk ID	TR-37
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Incorrect Billing Record
Description	Billing information may be recorded incorrectly.
Refinement/Context	Incorrect billing records may result in inaccurate transaction information.
Mitigation/Monitoring	Test billing calculations and verify that billing records are correctly stored and displayed.
Management/Contingency Plan/Trigger	If an incorrect billing record is found, correct the affected transaction and retest the billing process.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta – Technical Developer

Table 117: *RIS item No.37 Technical Risk*

Risk ID	TR-38
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Duplicate Transaction Records
Description	A transaction may be recorded more than once.
Refinement/Context	Duplicate records may cause inaccurate transaction history and billing information.
Mitigation/Monitoring	Test transaction processing and database operations to identify duplicate record creation.
Management/Contingency Plan/Trigger	If a duplicate transaction is found, identify the cause, remove or correct the duplicate record, and retest the transaction process.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 118: *RIS item No.38 Technical Risk*

Risk ID	TR-39
Date	21-Sep-26
Probability	81–99% (Very High)
Impact	High
Priority	1
Risk Name	Missing Transaction Records
Description	Completed transactions may not be properly recorded in the database.
Refinement/Context	Missing transaction records may result in incomplete transaction history and inaccurate reports.
Mitigation/Monitoring	Test transaction processing and verify that completed transactions are stored correctly.
Management/Contingency Plan/Trigger	If a transaction is missing, investigate the database operation, restore the record when possible, and correct the affected function.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta

Table 119: *RIS item No.39 Technical Risk*

Risk ID	TR-40
Date	21-Sep-26
Probability	61–80% (High)
Impact	Medium
Priority	2
Risk Name	Incorrect Date and Time Handling
Description	Dates or times may be stored or displayed incorrectly.
Refinement/Context	Incorrect date and time information may affect bookings, transactions, schedules, and records.
Mitigation/Monitoring	Test date and time fields using different valid values and verify their storage and display.
Management/Contingency Plan/Trigger	If date or time errors occur, correct the affected logic or configuration and retest related functions.
Current Status	Monitoring
Originator	Project Team
Assigned	Junray Alfanta – Technical Developer

Table 120: *RIS item No.40 Technical Risk*

Risk ID	TR-41
Date	21-Sep-26
Probability	41–60%
Impact	Medium
Priority	3
Risk Name	File Upload Failure
Description	Required files may fail to upload or be stored properly.
Refinement/Context	Required files may fail because of file size, file type, storage, or connection problems.
Mitigation/Monitoring	Test allowed file types, size limits, upload functions, and storage.
Management/Contingency Plan/Trigger	If an upload fails, identify the cause, retry using an allowed format, and correct the upload configuration if needed.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 121: *RIS item No.41 Technical Risk*

Risk ID	TR-42
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Database Backup Corruption
Description	A database backup may become corrupted and unusable.
Refinement/Context	A corrupted backup may prevent the restoration of important system and transaction data.
Mitigation/Monitoring	Perform scheduled database backups and verify backup integrity through regular restore tests.
Management/Contingency Plan/Trigger	If corruption occurs, use the latest verified backup, create a replacement backup, and restore and test the database if necessary.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 122: *RIS item No.42 Technical Risk*

Risk ID	TR-43
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Slow Database Queries
Description	Inefficient database queries may slow down system operations.
Refinement/Context	Complex or inefficient queries may cause delays when retrieving customer, product, service, or transaction records.
Mitigation/Monitoring	Review query performance, test frequently used queries, and optimize queries where necessary.
Management/Contingency Plan/Trigger	If slow queries are identified, optimize the affected queries and retest system performance.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 123: *RIS item No.43 Technical Risk*

Risk ID	TR-44
Date	21-Sep-26
Probability	61–80%
Impact	High
Priority	2
Risk Name	Hosting Configuration Failure
Description	Incorrect hosting configuration may prevent the system from operating correctly.
Refinement/Context	Incorrect hosting settings may cause application errors or prevent the deployed system from working properly.
Mitigation/Monitoring	Review hosting configuration and test the system after deployment or configuration changes.
Management/Contingency Plan/Trigger	If the system fails because of hosting settings, correct the configuration, redeploy if necessary, and retest the system.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 124: *RIS item No.44 Technical Risk*

Risk ID	TR-45
Date	21-Sep-26
Probability	41–60%
Impact	Medium
Priority	3
Risk Name	Domain Configuration Problem
Description	Domain configuration issues may prevent users from accessing the system.
Refinement/Context	Incorrect domain or DNS settings may make the web-based system unavailable through its assigned domain.
Mitigation/Monitoring	Verify domain and DNS configuration and monitor system accessibility after changes.
Management/Contingency Plan/Trigger	If the domain cannot access the system, correct the domain or DNS settings and verify access after propagation.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 125: *RIS item No.45 Technical Risk*

Risk ID	TR-46
Date	21-Sep-26
Probability	61–80%
Impact	High
Priority	2
Risk Name	HTTPS/SSL Configuration Problem
Description	Incorrect SSL configuration may cause security warnings or connection problems.
Refinement/Context	SSL or HTTPS configuration problems may prevent secure access or display browser security warnings.
Mitigation/Monitoring	Verify SSL certificate configuration, HTTPS settings, and certificate validity before deployment.
Management/Contingency Plan/Trigger	If SSL problems occur, correct the certificate or HTTPS configuration, renew the certificate if needed, and retest secure access.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 126: *RIS item No.46 Technical Risk*

Risk ID	TR-47
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Cross-Browser Display Error
Description	System pages may display incorrectly in different browsers.
Refinement/Context	Differences between browsers may affect page layout, styling, or system functions.
Mitigation/Monitoring	Test important pages and functions using the supported web browsers.
Management/Contingency Plan/Trigger	If display errors occur, correct CSS, layout, or browser-specific issues and retest across browsers.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 127: *RIS item No.47 Technical Risk*

Risk ID	TR-48
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Responsive Design Failure
Description	System pages may not display properly on different screen sizes.
Refinement/Context	Users may experience layout or usability problems when accessing the system on different screen sizes.
Mitigation/Monitoring	Test system pages on desktop, tablet, and mobile screen sizes.
Management/Contingency Plan/Trigger	If responsive problems occur, adjust the responsive layout and CSS and retest the affected pages.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 128: *RIS item No.48 Technical Risk*

Risk ID	TR-49
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Deployment Failure
Description	The system may fail during deployment to the hosting environment.
Refinement/Context	Deployment may fail because of incorrect configuration, missing files, dependencies, or environment differences.
Mitigation/Monitoring	Use a deployment checklist, test the system before deployment, and keep a backup of the working version.
Management/Contingency Plan/Trigger	If deployment fails, restore the previous working version, identify and correct the deployment issue, then redeploy and test the system.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 129: *RIS item No.49 Technical Risk*

Risk ID	TR-50
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	System Integration Failure
Description	Different system components may fail to work together correctly.
Refinement/Context	Problems between system modules, database functions, and application components may cause incorrect or incomplete system operations.
Mitigation/Monitoring	Perform integration testing between major system modules and verify data flow between components.
Management/Contingency Plan/Trigger	If integration fails, isolate the affected component, correct the interface or data flow, and perform full integration testing again.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 130: *RIS item No.50 Technical Risk*

Business Risks			
Risk ID	**Risk Name**	**Description**	**Priority**
BR-01	Low User Adoption	Users may not adopt the new web-based system as expected.	2
BR-02	Customer Resistance	Customers may prefer the existing manual process instead of using the system.	2
BR-03	Business Process Misalignment	The system may not properly match the existing business processes of ExGen.	1
BR-04	Budget Constraints	Available resources may be insufficient to support the project.	2
BR-05	Change in Management	Changes in management may affect project decisions or system use.	2
BR-06	Low Business Impact	The system may not improve business operations as expected.	2
BR-07	Changes in Business Requirements	Business needs may change during or after system development.	1

BR-08	Data Privacy Violation	Customer or business information may be exposed or handled improperly.	1
BR-09	Loss of Important Business Files	Important business records may be lost.	1
BR-10	Poor User Training	Staff may not receive sufficient training to use the system properly.	2
BR-11	Internet Dependency	Unreliable internet access may affect system availability.	2
BR-12	Negative User Feedback	Users may provide negative feedback because of system problems or difficulties.	2
BR-13	Delayed Project Delivery	Delays in project implementation may affect the intended business use of the system.	2
BR-14	Weak Technical Support	Technical issues may take too long to resolve because of limited support.	2
BR-15	Major Data Breach	Unauthorized access may expose important customer or business data.	1

BR-16	Limited Future Growth	The system may not adequately support future business needs.	2
BR-17	Incorrect Product Pricing	Incorrect product prices may appear in quotations or transactions.	1
BR-18	Outdated Product Information	Product details may not be updated when changes occur.	2
BR-19	Outdated Service Information	Service details may not be updated when changes occur.	2
BR-20	Incorrect Service Charges	Service charges may be recorded or displayed incorrectly.	1
BR-21	Inaccurate Business Rules	System business rules may not correctly reflect actual business operations.	1
BR-22	Customer Complaint	Customers may submit complaints because of incorrect or delayed transactions.	2
BR-23	Customer Information Error	Customer information may be entered or recorded incorrectly.	2
BR-24	Incorrect Customer Contact Information	Customer contact details may be recorded incorrectly.	2

BR-25	Inaccurate Vehicle Information	Customer vehicle information may be entered or recorded incorrectly.	2
BR-26	Incorrect Quotation Information	Quotation details may contain incorrect information.	1
BR-27	Billing Dispute	A customer may dispute the amount or information shown on a billing record.	2
BR-28	Quotation Dispute	A customer may dispute the information or amount shown in a quotation.	2
BR-29	Unclear Pricing Information	Customers may not clearly understand product or service pricing.	2
BR-30	Inconsistent Service Availability	Service availability information may not accurately reflect actual availability.	2
BR-31	Product Stock Information Not Updated	Product stock information may not be updated when inventory changes.	1
BR-32	Service Schedule Conflict	Multiple bookings may conflict with the available service schedule.	1

BR-33	Overbooking	The system may accept more service bookings than the business can accommodate.	1
BR-34	Missed Service Booking	A confirmed service booking may not be properly handled.	2
BR-35	Delayed Customer Response	Customer inquiries or requests may not receive a timely response.	2
BR-36	Customer Cancellation	A customer may cancel a previously requested or scheduled service.	3
BR-37	Customer No-Show	A customer may fail to appear for a scheduled service.	3
BR-38	Unauthorized Business Record Access	Unauthorized users may gain access to business records.	1
BR-39	Incorrect Staff Access	Staff members may be given incorrect system access permissions.	1
BR-40	Employee Error	Staff may make errors while entering or processing business information.	2
BR-41	Staff Resistance to New Workflow	Staff may be unwilling to adopt the new system workflow.	2

BR-42	Failure to Update Business Records	Business records may not be updated when changes occur.	2
BR-43	Inconsistent Manual and Digital Records	Manual and digital records may contain different information.	1
BR-44	Loss of Customer Trust	System errors may reduce customer confidence in the business.	2
BR-45	Poor Customer Experience	Customers may find the system process difficult or confusing.	2
BR-46	Incorrect Business Reports	Generated business reports may contain inaccurate information.	2
BR-47	Incomplete Transaction History	Important transaction records may be incomplete.	1
BR-48	Business Continuity Problem	Business operations may be affected when the system is unavailable.	1
BR-49	Increased Operating Cost	System maintenance or operation may create additional costs.	2
BR-50	Failure to Maintain System Information	Product, service, pricing, and business records may not be properly maintained.	2

Table 131: *RMMM Traceability for Technical Risk*

Risk ID	BR-01
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Low User Adoption
Description	Users may not adopt the new web-based system as expected.
Refinement/Context	Users may continue using familiar manual processes instead of regularly using the new system.
Mitigation/Monitoring	Introduce the system gradually, provide simple instructions, and monitor user usage and feedback.
Management/Contingency Plan/Trigger	If adoption remains low, identify user concerns, provide additional guidance, and adjust the system or process where needed.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 132: *RIS item No.1 Business Risk*

Risk ID	BR-02
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Customer Resistance
Description	Customers may prefer the existing manual process instead of using the system.
Refinement/Context	Some customers may be unfamiliar with the web-based process or prefer direct/manual transactions.
Mitigation/Monitoring	Provide clear instructions and make the quotation and booking process simple for customers.
Management/Contingency Plan/Trigger	If customers resist the system, collect feedback and provide assistance or maintain an appropriate manual alternative when necessary.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta – Business Analyst

Table 133: *RIS item No.2 Business Risk*

Risk ID	BR-03
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Business Process Misalignment
Description	The system may not properly match the existing business processes of ExGen.
Refinement/Context	System functions may differ from the actual quotation, billing, product, or service processes used by the business.
Mitigation/Monitoring	Review business processes with the client and validate system functions against approved requirements.
Management/Contingency Plan/Trigger	If a mismatch is identified, review the affected process and revise the system requirements or workflow with client approval.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 134: *RIS item No.3 Business Risk*

Risk ID	BR-04
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Budget Constraints
Description	Available resources may be insufficient to support the project.
Refinement/Context	Limited funds may affect hosting, development resources, testing, or other project needs.
Mitigation/Monitoring	Monitor project expenses and prioritize necessary resources within the approved budget.
Management/Contingency Plan/Trigger	If resources become insufficient, review expenses, prioritize essential activities, and adjust non-critical project needs.
Current Status	Open
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 135: *RIS item No.4 Business Risk*

Risk ID	BR-05
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Change in Management
Description	Changes in management may affect project decisions or system use.
Refinement/Context	New management may introduce different priorities or expectations for the system.
Mitigation/Monitoring	Document approved requirements, decisions, and business processes for continuity.
Management/Contingency Plan/Trigger	If management changes, review the project documentation with the new decision makers and confirm approved requirements.
Current Status	Open
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 136: *RIS item No.5 Business Risk*

Risk ID	BR-06
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Low Business Impact
Description	The system may not improve business operations as expected.
Refinement/Context	The implemented system may not provide sufficient improvement to the quotation, billing, booking, or record management processes.
Mitigation/Monitoring	Review expected business benefits and evaluate system functions against identified business needs.
Management/Contingency Plan/Trigger	If expected improvements are not achieved, identify affected processes and discuss appropriate system adjustments with the client.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 137: *RIS item No.6 Business Risk*

Risk ID	BR-07
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Changes in Business Requirements
Description	Business needs may change during or after system development.
Refinement/Context	Changes in products, services, pricing, or business procedures may require changes to system requirements.
Mitigation/Monitoring	Regularly review requirements with the client and document approved changes.
Management/Contingency Plan/Trigger	If business requirements change, evaluate the effect, obtain client approval, and update affected system functions and documentation.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 138: *RIS item No.7 Business Risk*

Risk ID	BR-08
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Data Privacy Violation
Description	Customer or business information may be exposed or handled improperly.
Refinement/Context	Sensitive customer and business records may be accessed, stored, or processed incorrectly.
Mitigation/Monitoring	Apply appropriate access controls, protect stored information, and review how customer and business data are handled.
Management/Contingency Plan/Trigger	If a privacy issue occurs, restrict affected access, investigate the incident, correct the problem, and review data protection procedures.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 139: *RIS item No.8 Business Risk*

Risk ID	BR-09
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Loss of Important Business Files
Description	Important business records may be lost.
Refinement/Context	Loss of quotations, billing records, customer information, or other business files may affect operations.
Mitigation/Monitoring	Perform regular backups and organize important business files and records properly.
Management/Contingency Plan/Trigger	If files are lost, recover them from the latest available backup and verify the restored records.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 140: *RIS item No.9 Business Risk*

Risk ID	BR-10
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Poor User Training
Description	Staff may not receive sufficient training to use the system properly.
Refinement/Context	Insufficient training may result in incorrect data entry, processing errors, or difficulty using system functions.
Mitigation/Monitoring	Provide user orientation, simple instructions, and demonstrations of important system functions.
Management/Contingency Plan/Trigger	If users experience difficulties, provide additional training and guidance on the affected functions.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 141: *RIS item No.10 Business Risk*

Risk ID	BR-11
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Internet Dependency
Description	Unreliable internet access may affect system availability.
Refinement/Context	The web-based system requires internet connectivity for users to access system functions.
Mitigation/Monitoring	Test system accessibility and identify reliable internet requirements for system use.
Management/Contingency Plan/Trigger	If internet access becomes unavailable, use an appropriate temporary manual process and resume system transactions when connectivity returns.
Current Status	Open
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 142: *RIS item No.11 Business Risk*

Risk ID	BR-12
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Negative User Feedback
Description	Users may provide negative feedback because of system problems or difficulties.
Refinement/Context	User dissatisfaction may result from confusing processes, errors, or system limitations.
Mitigation/Monitoring	Collect user feedback during testing and review reported problems regularly.
Management/Contingency Plan/Trigger	If repeated negative feedback occurs, identify the common issues and prioritize appropriate improvements.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 143: *RIS item No.12 Business Risk*

Risk ID	BR-13
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Delayed Project Delivery
Description	Delays in project implementation may affect the intended business use of the system.
Refinement/Context	Delayed development or deployment may prevent the business from using the planned system on time.
Mitigation/Monitoring	Monitor project milestones, task completion, and development progress regularly.
Management/Contingency Plan/Trigger	If project delivery is delayed, identify the cause, prioritize critical tasks, and adjust the schedule as necessary.
Current Status	Open
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 144: *RIS item No.13 Business Risk*

Risk ID	BR-14
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Weak Technical Support
Description	Technical issues may take too long to resolve because of limited support.
Refinement/Context	Users may experience extended problems when technical assistance is unavailable or delayed.
Mitigation/Monitoring	Document common technical issues and establish a process for reporting problems.
Management/Contingency Plan/Trigger	If a technical issue occurs, assign it to the responsible technical member, investigate the cause, and apply the appropriate fix.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 145: *RIS item No.14 Business Risk*

Risk ID	BR-15
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Major Data Breach
Description	Unauthorized access may expose important customer or business data.
Refinement/Context	A security incident may expose customer information, transaction records, or business information.
Mitigation/Monitoring	Apply authentication, authorization, secure database access, and regular security checks.
Management/Contingency Plan/Trigger	If a breach occurs, restrict unauthorized access, investigate the affected records, correct the security weakness, and review access controls.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 146: *RIS item No.15 Business Risk*

Risk ID	BR-16
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Limited Future Growth
Description	The system may not adequately support future business needs.
Refinement/Context	Increased products, services, customers, or transactions may require additional system capabilities.
Mitigation/Monitoring	Consider future business needs during system design and keep system records and functions organized.
Management/Contingency Plan/Trigger	If future needs exceed current capabilities, identify required improvements and plan system enhancements.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 147: *RIS item No.16 Business Risk*

Risk ID	BR-17
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Incorrect Product Pricing
Description	Incorrect product prices may appear in quotations or transactions.
Refinement/Context	Incorrect product prices may result in inaccurate quotations or billing information.
Mitigation/Monitoring	Verify product prices with the client and review pricing information before use.
Management/Contingency Plan/Trigger	If incorrect pricing is found, correct the product information and review affected quotations or transactions.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 148: *RIS item No.17 Business Risk*

Risk ID	BR-18
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Outdated Product Information
Description	Product details may not be updated when changes occur.
Refinement/Context	Old product names, descriptions, prices, or availability may remain in the system.
Mitigation/Monitoring	Regularly review product records and confirm updates with authorized business personnel.
Management/Contingency Plan/Trigger	If outdated information is identified, update the affected product records and verify the changes.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 149: *RIS item No.18 Business Risk*

Risk ID	BR-19
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Outdated Service Information
Description	Service details may not be updated when changes occur.
Refinement/Context	Old service descriptions, charges, or availability may remain in the system.
Mitigation/Monitoring	Regularly review service information and confirm updates with authorized business personnel.
Management/Contingency Plan/Trigger	If outdated service information is identified, update the affected records and verify the changes.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 150: *RIS item No.19 Business Risk*

Risk ID	BR-20
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Incorrect Service Charges
Description	Service charges may be recorded or displayed incorrectly.
Refinement/Context	Incorrect service charges may result in inaccurate quotations or billing records.
Mitigation/Monitoring	Verify service charges with the client and test quotation and billing calculations.
Management/Contingency Plan/Trigger	If incorrect charges are identified, correct the service information and review affected quotations or billing records.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 151: *RIS item No.20 Business Risk*

Risk ID	BR-21
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Inaccurate Business Rules
Description	System business rules may not correctly reflect actual business operations.
Refinement/Context	System rules for quotations, services, bookings, or billing may differ from actual ExGen procedures.
Mitigation/Monitoring	Review business rules with the client and validate them against actual business processes.
Management/Contingency Plan/Trigger	If incorrect rules are identified, revise the affected requirements or system logic with client approval.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 152: *RIS item No.21 Business Risk*

Risk ID	BR-22
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Customer Complaint
Description	Customers may submit complaints because of incorrect or delayed transactions.
Refinement/Context	Errors in quotations, bookings, billing, or customer records may lead to complaints.
Mitigation/Monitoring	Monitor customer feedback and review transaction errors regularly.
Management/Contingency Plan/Trigger	If a complaint occurs, investigate the transaction, correct the issue, and communicate the appropriate resolution.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 153: *RIS item No.22 Business Risk*

Risk ID	BR-23
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Customer Information Error
Description	Customer information may be entered or recorded incorrectly.
Refinement/Context	Incorrect customer information may affect quotations, bookings, billing, and transaction records.
Mitigation/Monitoring	Use form validation and review customer information during testing and processing.
Management/Contingency Plan/Trigger	If incorrect information is found, correct the customer record and review affected transactions.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 154: *RIS item No.23 Business Risk*

Risk ID	BR-24
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Incorrect Customer Contact Information
Description	Customer contact details may be recorded incorrectly.
Refinement/Context	Incorrect phone numbers, email addresses, or other contact information may prevent proper communication.
Mitigation/Monitoring	Validate required contact fields and review customer information for accuracy.
Management/Contingency Plan/Trigger	If incorrect contact information is found, correct the customer record and verify the updated details.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 155: *RIS item No.24 Business Risk*

Risk ID	BR-25
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Inaccurate Vehicle Information
Description	Customer vehicle information may be entered or recorded incorrectly.
Refinement/Context	Incorrect vehicle details may affect service selection, booking, and customer records.
Mitigation/Monitoring	Validate vehicle information fields and test vehicle data recording and display.
Management/Contingency Plan/Trigger	If incorrect vehicle information is identified, correct the record and verify affected service or booking information.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 156: *RIS item No.25 Business Risk*

Risk ID	BR-26
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Incorrect Quotation Information
Description	Quotation details may contain incorrect information.
Refinement/Context	Incorrect product, service, customer, or pricing information may appear in quotations.
Mitigation/Monitoring	Test quotation generation and verify customer, product, service, and pricing information.
Management/Contingency Plan/Trigger	If incorrect quotation information is found, correct the source data or calculation and regenerate the quotation.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 157: *RIS item No.26 Business Risk*

Risk ID	BR-27
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Billing Dispute
Description	A customer may dispute the amount or information shown on a billing record.
Refinement/Context	Billing disputes may occur when charges do not match the agreed quotation or actual transaction.
Mitigation/Monitoring	Verify billing information and compare billing records with approved quotations and transactions.
Management/Contingency Plan/Trigger	If a billing dispute occurs, review the transaction and correct the billing record if an error is confirmed.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 158: *RIS item No.27 Business Risk*

Risk ID	BR-28
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Quotation Dispute
Description	A customer may dispute the information or amount shown in a quotation.
Refinement/Context	Quotation disputes may occur because of incorrect prices, services, products, or customer information.
Mitigation/Monitoring	Review quotation details and verify prices and selected services before finalizing quotations.
Management/Contingency Plan/Trigger	If a quotation is disputed, review the source information and correct and regenerate the quotation if necessary.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 159: *RIS item No.28 Business Risk*

Risk ID	BR-29
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Unclear Pricing Information
Description	Customers may not clearly understand product or service pricing.
Refinement/Context	Unclear prices or charges may cause confusion during quotation and transaction processes.
Mitigation/Monitoring	Display product and service prices clearly and review pricing information with the client.
Management/Contingency Plan/Trigger	If customers report unclear pricing, improve the presentation and clarify the affected pricing information.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 160: *RIS item No.29 Business Risk*

Risk ID	BR-30
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Inconsistent Service Availability
Description	Service availability information may not accurately reflect actual availability.
Refinement/Context	The system may show services as available when the business cannot provide them at the requested time.
Mitigation/Monitoring	Regularly review service availability and compare system information with actual business availability.
Management/Contingency Plan/Trigger	If availability information is incorrect, update the affected records and review related bookings.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 161: *RIS item No.30 Business Risk*

Risk ID	BR-31
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Product Stock Information Not Updated
Description	Product stock information may not be updated when inventory changes.
Refinement/Context	Outdated stock information may cause products to appear available when they are unavailable.
Mitigation/Monitoring	Regularly update product stock information and verify inventory records.
Management/Contingency Plan/Trigger	If stock information is incorrect, update the product record and review affected quotations or transactions.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 162: *RIS item No.31 Business Risk*

Risk ID	BR-32
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Service Schedule Conflict
Description	Multiple bookings may conflict with the available service schedule.
Refinement/Context	Overlapping service schedules may cause delays or prevent the business from handling confirmed bookings.
Mitigation/Monitoring	Test booking schedules and verify that available time slots are properly managed.
Management/Contingency Plan/Trigger	If a schedule conflict occurs, review affected bookings, coordinate with the customer, and adjust the schedule when necessary.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 163: *RIS item No.32 Business Risk*

Risk ID	BR-33
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Overbooking
Description	The system may accept more service bookings than the business can accommodate.
Refinement/Context	Too many bookings for the same service period may exceed available staff, time, or service capacity.
Mitigation/Monitoring	Define booking limits and test the system's handling of service capacity.
Management/Contingency Plan/Trigger	If overbooking occurs, identify affected bookings, coordinate with customers, and adjust schedules based on available capacity.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 164: *RIS item No.33 Business Risk*

Risk ID	BR-34
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Missed Service Booking
Description	A confirmed service booking may not be properly handled.
Refinement/Context	A booking may be overlooked, incorrectly recorded, or not communicated to the staff responsible for the service.
Mitigation/Monitoring	Review confirmed bookings and verify that booking information is properly recorded and accessible.
Management/Contingency Plan/Trigger	If a booking is missed, verify the record, inform the responsible staff, and coordinate with the customer for an appropriate schedule.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 165: *RIS item No.34 Business Risk*

Risk ID	BR-35
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Delayed Customer Response
Description	Customer inquiries or requests may not receive a timely response.
Refinement/Context	Delayed responses may affect customer satisfaction and service scheduling.
Mitigation/Monitoring	Monitor customer inquiries and establish a process for handling requests within an appropriate time.
Management/Contingency Plan/Trigger	If responses are delayed, prioritize pending inquiries and review the cause of the delay.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 166: *RIS item No.35 Business Risk*

Risk ID	BR-36
Date	21-Sep-26
Probability	41–60%
Impact	Medium
Priority	3
Risk Name	Customer Cancellation
Description	A customer may cancel a previously requested or scheduled service.
Refinement/Context	Customer cancellations may create unused service schedules or affect expected transactions.
Mitigation/Monitoring	Record cancellation information and monitor booking status accurately.
Management/Contingency Plan/Trigger	If a customer cancels, update the booking status and make the service schedule available when appropriate.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 167: *RIS item No.36 Business Risk*

Risk ID	BR-37
Date	21-Sep-26
Probability	41–60%
Impact	Medium
Priority	3
Risk Name	Customer No-Show
Description	A customer may fail to appear for a scheduled service.
Refinement/Context	A no-show may leave an unused service slot and affect daily service scheduling.
Mitigation/Monitoring	Monitor confirmed bookings and provide appropriate booking reminders when possible.
Management/Contingency Plan/Trigger	If a customer does not appear, update the booking status and make the schedule available for other activities when appropriate.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 168: *RIS item No.37 Business Risk*

Risk ID	BR-38
Date	21-Sep-26
Probability	81–99%
Impact	High

Priority	1
Risk Name	Unauthorized Business Record Access
Description	Unauthorized users may gain access to business records.
Refinement/Context	Unauthorized access may expose customer, quotation, billing, product, or service records.
Mitigation/Monitoring	Apply user authentication, role-based access, and regular access permission reviews.
Management/Contingency Plan/Trigger	If unauthorized access is detected, restrict the account or access, investigate the incident, and correct the permission settings.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 169: *RIS item No.38 Business Risk*

Risk ID	BR-39
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Incorrect Staff Access
Description	Staff members may be given incorrect system access permissions.
Refinement/Context	Staff may receive access to functions or records that are not appropriate for their responsibilities.
Mitigation/Monitoring	Define user roles and test access permissions before system use.
Management/Contingency Plan/Trigger	If incorrect access is identified, update the staff account permissions and retest access controls.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 170: *RIS item No.39 Business Risk*

Risk ID	BR-40
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Employee Error
Description	Staff may make errors while entering or processing business information.
Refinement/Context	Incorrect data entry or processing may affect customer, product, service, quotation, or billing records.
Mitigation/Monitoring	Provide user training, input validation, and clear system instructions.
Management/Contingency Plan/Trigger	If an employee error occurs, correct the affected record and provide additional guidance when necessary.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 171: *RIS item No.40 Business Risk*

Risk ID	BR-41
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Staff Resistance to New Workflow
Description	Staff may be unwilling to adopt the new system workflow.
Refinement/Context	Staff may prefer existing manual procedures and may be hesitant to change their usual work process.
Mitigation/Monitoring	Explain the new workflow, provide training, and collect staff feedback during implementation.
Management/Contingency Plan/Trigger	If resistance continues, identify concerns, provide additional guidance, and review workflow improvements with the client.
Current Status	Open
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 172: *RIS item No.41 Business Risk*

Risk ID	BR-42
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Failure to Update Business Records
Description	Business records may not be updated when changes occur.
Refinement/Context	Outdated customer, product, service, pricing, or transaction information may remain in the system.
Mitigation/Monitoring	Assign responsibility for maintaining business records and review information regularly.
Management/Contingency Plan/Trigger	If records are not updated, identify outdated information, assign the update task, and verify the corrected records.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 173: *RIS item No.42 Business Risk*

Risk ID	BR-43
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Inconsistent Manual and Digital Records
Description	Manual and digital records may contain different information.
Refinement/Context	Differences between manual records and system records may cause confusion and inaccurate business information.
Mitigation/Monitoring	Compare important manual and digital records during transition and maintain a consistent update process.
Management/Contingency Plan/Trigger	If records do not match, identify the correct information, update the affected record, and verify consistency.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 174: *RIS item No.43 Business Risk*

Risk ID	BR-44
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Loss of Customer Trust
Description	System errors may reduce customer confidence in the business.
Refinement/Context	Repeated quotation, billing, booking, or information errors may affect customer confidence.
Mitigation/Monitoring	Monitor transaction accuracy, resolve customer concerns promptly, and test important system functions.
Management/Contingency Plan/Trigger	If customer confidence is affected, investigate the cause, correct errors, and improve the affected process.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 175: *RIS item No.44 Business Risk*

Risk ID	BR-45
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Poor Customer Experience
Description	Customers may find the system process difficult or confusing.
Refinement/Context	Complex navigation, unclear information, or difficult quotation and booking processes may affect customer experience.
Mitigation/Monitoring	Conduct usability testing and collect feedback from users during system evaluation.
Management/Contingency Plan/Trigger	If customers experience difficulties, identify confusing parts of the process and improve the affected interface or instructions.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 176: *RIS item No.45 Business Risk*

Risk ID	BR-46
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Incorrect Business Reports
Description	Generated business reports may contain inaccurate information.
Refinement/Context	Incorrect or incomplete database records may result in inaccurate reports.
Mitigation/Monitoring	Test report generation and compare reports with source transaction and business records.
Management/Contingency Plan/Trigger	If inaccurate reports are identified, check the source data and report logic, correct the issue, and regenerate the report.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 177: *RIS item No.46 Business Risk*

Risk ID	BR-47
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Incomplete Transaction History
Description	Important transaction records may be incomplete.
Refinement/Context	Missing transaction information may affect billing, reporting, and business record keeping.
Mitigation/Monitoring	Test transaction recording and regularly review stored transaction information.
Management/Contingency Plan/Trigger	If transaction records are incomplete, investigate the missing information, recover available records, and correct the affected data.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 178: *RIS item No.47 Business Risk*

Risk ID	BR-48
Date	21-Sep-26
Probability	81–99%
Impact	High
Priority	1
Risk Name	Business Continuity Problem
Description	Business operations may be affected when the system is unavailable.
Refinement/Context	System downtime may prevent staff from accessing customer, booking, quotation, or billing information.
Mitigation/Monitoring	Perform backups, monitor system availability, and prepare an appropriate temporary manual process.
Management/Contingency Plan/Trigger	If the system becomes unavailable, use the temporary manual process, restore system availability, and encode or verify affected records afterward.
Current Status	Open
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 179: *RIS item No.48 Business Risk*

Risk ID	BR-49
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Increased Operating Cost
Description	System maintenance or operation may create additional costs.
Refinement/Context	Hosting, maintenance, updates, or technical support may require costs beyond initial project expenses.
Mitigation/Monitoring	Monitor operating and maintenance expenses and consider required costs during planning.
Management/Contingency Plan/Trigger	If operating costs increase, review expenses, prioritize essential services, and adjust the budget when necessary.
Current Status	Open
Originator	Project Team
Assigned	Wane Summer J. Francisco

Table 180: *RIS item No.49 Business Risk*

Risk ID	BR-50
Date	21-Sep-26
Probability	61–80%
Impact	Medium
Priority	2
Risk Name	Failure to Maintain System Information
Description	Product, service, pricing, and business records may not be properly maintained.
Refinement/Context	Failure to regularly update system information may cause outdated or inaccurate business records.
Mitigation/Monitoring	Assign responsibility for maintaining system information and conduct regular record reviews.
Management/Contingency Plan/Trigger	If information is not maintained, identify outdated records, update them, and verify the information with authorized business personnel.
Current Status	Open
Originator	Project Team
Assigned	Junray Alfanta

Table 181: *RIS item No.50 Business Risk*

References

Autodesk. (2020, June 18). *Guide to successful project closeout*. Digital Builder. https://constructionblog.autodesk.com/project-closeout/

Beale, S. (2021, August 24). *5 steps to metrics collection and usage*. MasterControl. https://www.mastercontrol.com/gxp-lifeline/an-introduction-to-metrics-collection-and-usage/

Harned, B. (n.d.). *How to estimate project cost and time*. TeamGantt. Retrieved February 19, 2022, from https://www.teamgantt.com/project-management-guide/how-to-estimate-projects

LaPrad, L. (2018, July 10). *Project management reporting types & tips*. TeamGantt. https://www.teamgantt.com/blog/project-management-reporting-types-and-tips

Lopez, A. (2020, April 28). *How to make a process improvement plan*. ProjectManager.com. https://www.projectmanager.com/blog/process-improvement-plan

MasterClass. (2021, August 23). *What's the difference? Preface, prologue, introduction, and foreword*. MasterClass. https://www.masterclass.com/articles/preface-prologue-introduction-difference#want-to-learn-more-about-writing

Simmons, M. (2020, November 23). *What is a project deliverable? Definition, examples & more*. ProjectManager.com. https://www.teamgantt.com/blog/project-management-reporting-types-and-tips

Simmons, M. (2021, August 5). *Five essential tips for schedule control in project management*. ProjectManager.com. https://www.projectmanager.com/blog/schedule-control-tips

Sulemani, M. (2021, January 4). *What is a software process model?* Educative. https://www.educative.io/blog/software-process-model-types

Tarhanis, W. (2018, February 6). *Assumptions and constraints in project management*. Projectcubicle. https://www.projectcubicle.com/assumptions-and-constraints/

Wikipedia Contributors. (2021, March 19). *Resource (project management)*. Wikipedia. https://en.wikipedia.org/wiki/Resource_(project_management)

Wikipedia Contributors. (2021, July 26). *Risk management plan*. Wikipedia. https://en.wikipedia.org/wiki/Risk_management_plan

Wikipedia Contributors. (2022, February 7). *IT infrastructure*. Wikipedia. https://en.wikipedia.org/wiki/IT_infrastructure

Wood, D. C., & Furterer, S. L. (2020). *The ASQ certified manager of quality/organizational excellence handbook*. ASQ Quality Press.

Appendices

APPENDIX A

July 29, 2026

MR. WENDALE AJERO
Owner, Exgen Battery Center and Car Wash, Ozamiz City

Dear Mr. Wendale Ajero,

Good day!

We are writing to respectfully request your permission to use **Exgen Battery Center & Car Wash** as the subject of our research project entitled **"Exgen Battery Center & Car Wash: A Web-Based Management System for Inventory, Service Booking, and Customer Information,"** which is being conducted as part of our Software Engineering course requirements and may also serve as the foundation for our future Capstone Project.

In line with this, we respectfully request your permission to conduct an interview with you. Your insights will help us understand the current business processes of Exgen Battery Center & Car Wash and assist us in developing a web-based management system that will improve inventory management, streamline service booking, organize customer information, and enhance the overall efficiency of business operations.

Additionally, we would like to request your consent to record the interview for documentation and research purposes. The recording will be handled with strict confidentiality and will be used solely to ensure the accuracy of our findings.

If you have any questions or need further clarification regarding the interview, please feel free to contact us at **09108754074** or via email at **junray.alfanta@lsu.edu.ph**.

Your participation would be greatly appreciated and would significantly contribute to the success of our study.

Thank you for your time and consideration. We look forward to your positive response.

Respectfully,

JUNRAY T. ALFANTA
Researcher

WANE SUMMER J. FRANCISCO
Researcher

JEWEL NERISHA T. TOMALE
Researcher

Noted by:

8-1-2026

MR. HONIMAR C. PANGANIBAN, MSIT
Software Engineering for IT Professor

Approved by:

MR. WENDALE AJERO
Owner, Exgen Battery Center and Carwash

Figure 3: *Transmittal Letter*



Figure 4: *First Meeting with the Client*
